
Gantt Chart

200-Bed Hospital Construction (as-planned schedule, calculated by Planora)

The Gantt chart shows every task as a bar on a calendar. The hospital project starts on **4 Jan 2027** and finishes on **18 Oct 2028**: **467 working days**. Both charts below were exported directly from Planora with the critical path shown in red.

Phase summary

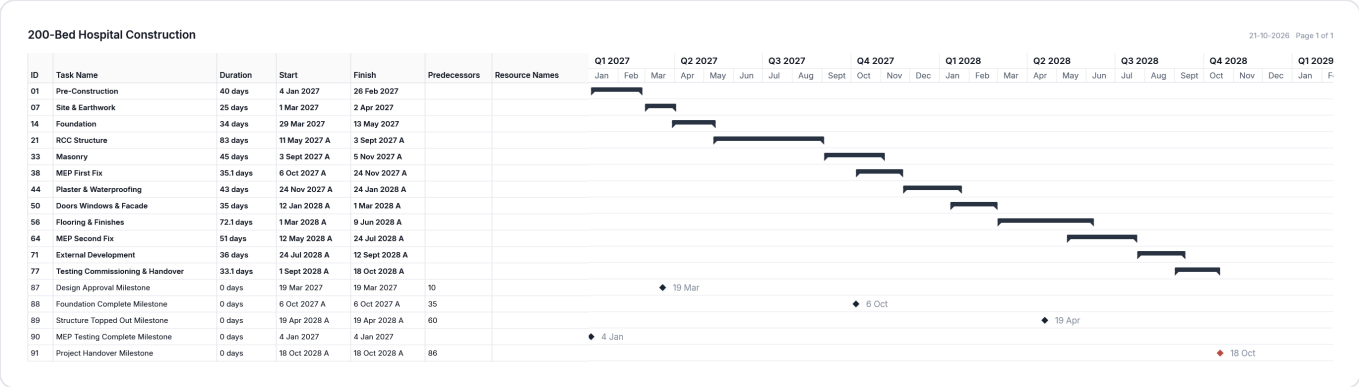

The 12 phases and 5 milestones (summary view).

Key dates

Milestone	Date
Design Approval Milestone	19 Mar 2027
Foundation Complete Milestone	6 Oct 2027
Structure Topped Out Milestone	19 Apr 2028
MEP Testing Complete Milestone	4 Jan 2027
Project Handover Milestone	18 Oct 2028


Three milestones in the source file are linked to unrelated tasks or a missing task (for example “MEP Testing Complete” points to task UID 100, which is not in the file), so their dates follow those links.

Detailed Gantt chart (all 91 tasks)

200-Bed Hospital Construction

21-10-2026 Page 1 of 1

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
01	**Pre-Construction**	**40 days**	**4 Jan 2027**	**26 Feb 2027**		
02	Site Survey & Soil Investigation	5 days	4 Jan 2027	8 Jan 2027		Project Manager
03	Architectural & Structural Design	10 days	11 Jan 2027	22 Jan 2027	2	Planning Engineer
04	Municipal Approvals	12 days	25 Jan 2027	9 Feb 2027	3	Civil Engineer
05	Tendering & Contractor Appointment	8 days	10 Feb 2027	19 Feb 2027	4	Site Supervisor
06	Site Mobilization	5 days	22 Feb 2027	26 Feb 2027	5	QA/QC Engineer
07	**Site & Earthwork**	**25 days**	**1 Mar 2027**	**2 Apr 2027**		
08	Site Clearing	4 days	1 Mar 2027	4 Mar 2027	6	Safety Officer
09	Setting Out	3 days	5 Mar 2027	9 Mar 2027	8	Electrical Team
10	Excavation	8 days	10 Mar 2027	19 Mar 2027	9	MEP Contractor
11	Earthwork Disposal	5 days	22 Mar 2027	26 Mar 2027	10	Project Manager
12	Dewatering	5 days	29 Mar 2027	2 Apr 2027	11	Planning Engineer
13	Backfilling & Compaction	6 days	19 Mar 2027	26 Mar 2027	12SF	Civil Engineer
14	**Foundation**	**34 days**	**29 Mar 2027**	**13 May 2027**		
15	PCC Bed	3 days	29 Mar 2027	31 Mar 2027	13	Site Supervisor
16	Pile Installation	12 days	1 Apr 2027	16 Apr 2027	15	QA/QC Engineer
17	Pile Testing	4 days	19 Apr 2027	22 Apr 2027	16	Safety Officer
18	Pile Caps	8 days	23 Apr 2027	4 May 2027	17	Electrical Team
19	Foundation Beams	7 days	5 May 2027	13 May 2027	18	MEP Contractor
20	Waterproofing	4 days	5 May 2027 A	11 May 2027 A	19SS+0.1 days	Project Manager
21	**RCC Structure**	**83 days**	**11 May 2027 A**	**3 Sept 2027 A**		
22	Ground Floor Columns	7 days	11 May 2027 A	20 May 2027 A	20	Planning Engineer
23	Ground Floor Beams & Slab	8 days	20 May 2027 A	1 Jun 2027 A	22	Civil Engineer
24	First Floor RCC	10 days	1 Jun 2027 A	15 Jun 2027 A	23	Site Supervisor
25	Second Floor RCC	10 days	15 Jun 2027 A	29 Jun 2027 A	24	QA/QC Engineer
26	Third Floor RCC	10 days	1 Jun 2027 A	15 Jun 2027 A	25SF	Safety Officer
27	Fourth Floor RCC	10 days	15 Jun 2027 A	29 Jun 2027 A	26	Electrical Team
28	Fifth Floor RCC	10 days	29 Jun 2027 A	13 Jul 2027 A	27	MEP Contractor
29	Sixth Floor RCC	10 days	13 Jul 2027 A	27 Jul 2027 A	28	Project Manager
30	Seventh Floor RCC	10 days	27 Jul 2027 A	10 Aug 2027 A	29	Planning Engineer
31	Eighth Floor RCC	10 days	10 Aug 2027 A	24 Aug 2027 A	30	Civil Engineer
32	Roof Slab & Parapet	8 days	24 Aug 2027 A	3 Sept 2027 A	31	Site Supervisor
33	**Masonry**	**45 days**	**3 Sept 2027 A**	**5 Nov 2027 A**		
34	Ground Floor Brickwork	8 days	3 Sept 2027 A	15 Sept 2027 A	32	QA/QC Engineer
35	Typical Floor Brickwork	15 days	15 Sept 2027 A	6 Oct 2027 A	34	Safety Officer
36	Internal Blockwork	12 days	6 Oct 2027 A	22 Oct 2027 A	35	Electrical Team
37	External Wall Masonry	10 days	22 Oct 2027 A	5 Nov 2027 A	36	MEP Contractor
38	**MEP First Fix**	**35.1 days**	**6 Oct 2027 A**	**24 Nov 2027 A**		
39	Electrical Conduits	12 days	6 Oct 2027 A	22 Oct 2027 A	37SF	Project Manager
40	Plumbing Pipework	10 days	6 Oct 2027 A	20 Oct 2027 A	39SS+0.1 days	Planning Engineer
41	Fire Fighting Pipework	10 days	20 Oct 2027 A	3 Nov 2027 A	40	Civil Engineer
42	HVAC Sleeves & Duct Supports	8 days	3 Nov 2027 A	15 Nov 2027 A	41	Site Supervisor
43	ELV & Data Conduits	7 days	15 Nov 2027 A	24 Nov 2027 A	42	QA/QC Engineer
44	**Plaster & Waterproofing**	**43 days**	**24 Nov 2027 A**	**24 Jan 2028 A**		
45	Internal Plaster	15 days	24 Nov 2027 A	15 Dec 2027 A	43	Safety Officer
46	External Plaster	12 days	15 Dec 2027 A	31 Dec 2027 A	45	Electrical Team
47	Toilet Waterproofing	8 days	31 Dec 2027 A	12 Jan 2028 A	46	MEP Contractor
48	Terrace Waterproofing	6 days	12 Jan 2028 A	20 Jan 2028 A	47	Project Manager
49	Water Ponding Test	2 days	20 Jan 2028 A	24 Jan 2028 A	48	Planning Engineer
50	**Doors Windows & Facade**	**35 days**	**12 Jan 2028 A**	**1 Mar 2028 A**		
51	Door Frames	7 days	24 Jan 2028 A	2 Feb 2028 A	49	Civil Engineer
52	Window Frames	8 days	12 Jan 2028 A	24 Jan 2028 A	51SF	Site Supervisor
53	Glass Installation	10 days	24 Jan 2028 A	7 Feb 2028 A	52	QA/QC Engineer
54	Aluminium Cladding	12 days	7 Feb 2028 A	23 Feb 2028 A	53	Safety Officer
55	Facade Sealant	5 days	23 Feb 2028 A	1 Mar 2028 A	54	Electrical Team
56	**Flooring & Finishes**	**72.1 days**	**1 Mar 2028 A**	**9 Jun 2028 A**		
57	Floor Screed	8 days	1 Mar 2028 A	13 Mar 2028 A	55	MEP Contractor
58	Tile Flooring	15 days	13 Mar 2028 A	3 Apr 2028 A	57	Project Manager
59	Wall Tiling	12 days	3 Apr 2028 A	19 Apr 2028 A	58	Planning Engineer
60	False Ceiling	12 days	3 Apr 2028 A	19 Apr 2028 A	59SS+0.1 days	Civil Engineer
61	Internal Painting	15 days	19 Apr 2028 A	10 May 2028 A	60	Site Supervisor
62	External Painting	10 days	10 May 2028 A	24 May 2028 A	61	QA/QC Engineer
63	Joinery & Cabinets	12 days	24 May 2028 A	9 Jun 2028 A	62	Safety Officer
64	**MEP Second Fix**	**51 days**	**12 May 2028 A**	**24 Jul 2028 A**		
65	Electrical Fixtures	8 days	12 May 2028 A	24 May 2028 A	63SF	Electrical Team
66	Plumbing Fixtures	7 days	24 May 2028 A	2 Jun 2028 A	65	MEP Contractor
67	Sanitary Fixtures	6 days	2 Jun 2028 A	12 Jun 2028 A	66	Project Manager
68	Fire Alarm Installation	5 days	12 Jun 2028 A	19 Jun 2028 A	67	Planning Engineer
69	HVAC Equipment	10 days	19 Jun 2028 A	3 Jul 2028 A	68	Civil Engineer
70	Lift Installation	15 days	3 Jul 2028 A	24 Jul 2028 A	69	Site Supervisor
71	**External Development**	**36 days**	**24 Jul 2028 A**	**12 Sept 2028 A**		
72	Compound Wall	10 days	24 Jul 2028 A	7 Aug 2028 A	70	QA/QC Engineer
73	Internal Roads	8 days	7 Aug 2028 A	17 Aug 2028 A	72	Safety Officer
74	Storm Water Drainage	7 days	17 Aug 2028 A	28 Aug 2028 A	73	Electrical Team
75	Landscaping	8 days	28 Aug 2028 A	7 Sept 2028 A	74	MEP Contractor
76	Parking Marking	3 days	7 Sept 2028 A	12 Sept 2028 A	75	Project Manager
77	**Testing Commissioning & Handover**	**33.1 days**	**1 Sept 2028 A**	**18 Oct 2028 A**		
78	Electrical Testing	4 days	1 Sept 2028 A	7 Sept 2028 A	76SF	Planning Engineer
79	Plumbing Pressure Test	3 days	7 Sept 2028 A	12 Sept 2028 A	78	Civil Engineer
80	Fire System Testing	4 days	7 Sept 2028 A	13 Sept 2028 A	79SS+0.1 days	Site Supervisor
81	HVAC Testing	5 days	13 Sept 2028 A	20 Sept 2028 A	80	QA/QC Engineer
82	Lift Testing	4 days	20 Sept 2028 A	26 Sept 2028 A	81	Safety Officer
83	Snag Inspection	5 days	26 Sept 2028 A	3 Oct 2028 A	82	Electrical Team
84	Snag Rectification	8 days	3 Oct 2028 A	13 Oct 2028 A	83	MEP Contractor
85	Final Client Inspection	2 days	13 Oct 2028 A	17 Oct 2028 A	84	Project Manager
86	Project Handover	1 day	17 Oct 2028 A	18 Oct 2028 A	85	Planning Engineer
87	Design Approval Milestone	0 days	19 Mar 2027	19 Mar 2027	10	
88	Foundation Complete Milestone	0 days	6 Oct 2027 A	6 Oct 2027 A	35	
89	Structure Topped Out Milestone	0 days	19 Apr 2028 A	19 Apr 2028 A	60	
90	MEP Testing Complete Milestone	0 days	4 Jan 2027	4 Jan 2027		
91	Project Handover Milestone	0 days	18 Oct 2028 A	18 Oct 2028 A	86	

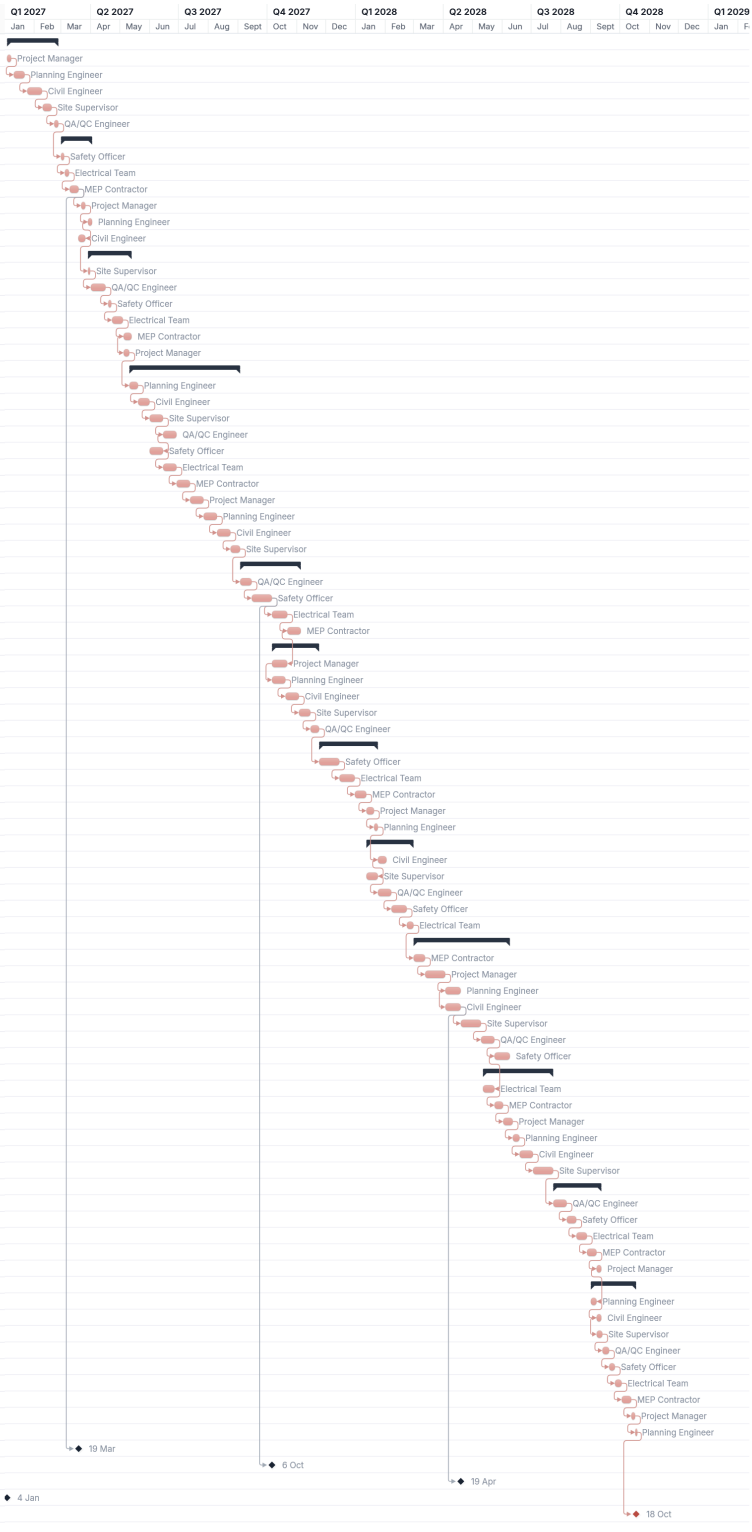

All phases and tasks with durations, dates, predecessors, resources and dependency arrows. Red = critical.
