
PLANORA

User Manual

Project scheduling and control: every feature explained, with a step-by-step tutorial for building, tracking and reporting a schedule.

Version	Platform	Edition
1.0.0	Windows 10 / 11 (64-bit)	October 2026

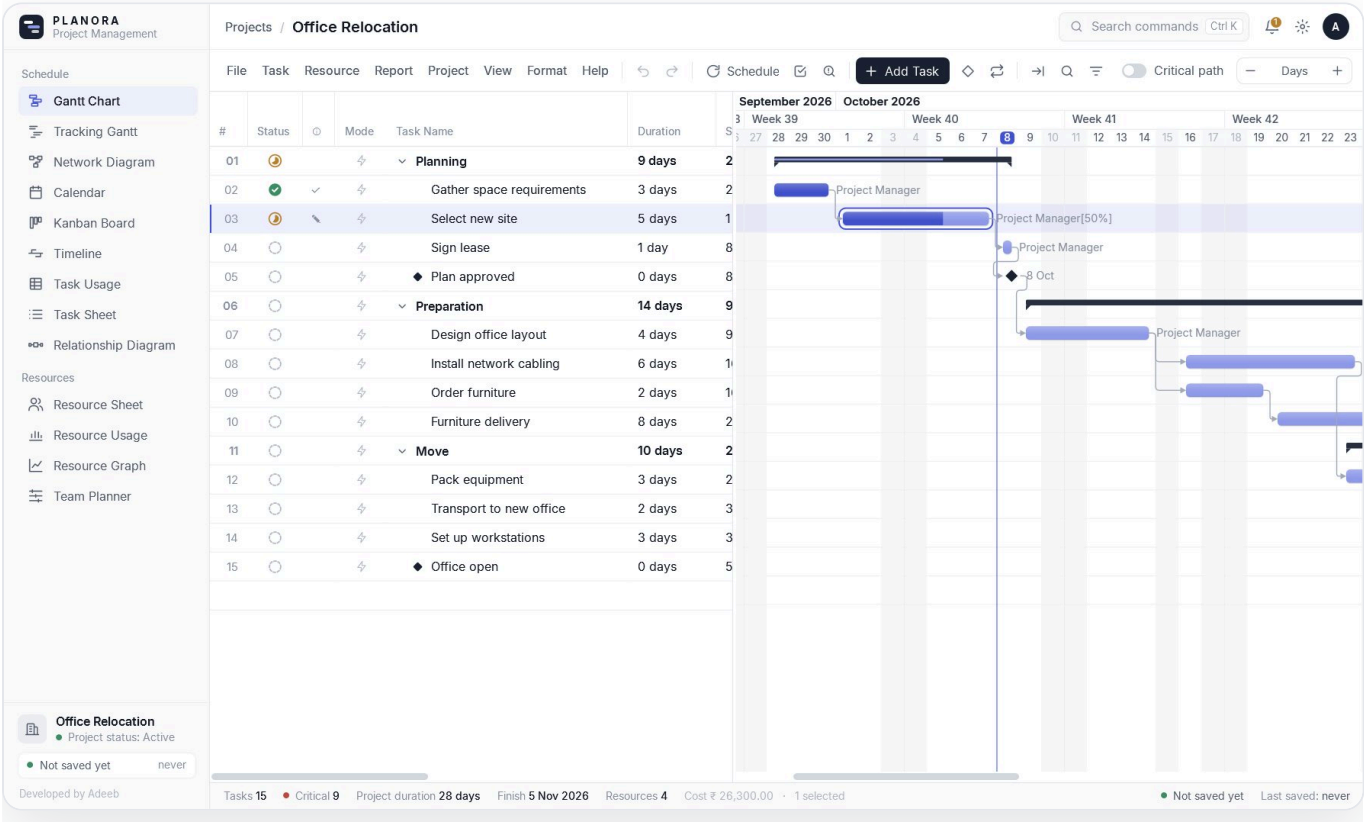

CONTENTS

What is in this manual

PART 1 · GETTING STARTED

1. Installing Planora
2. The Planora window
3. Command search (Ctrl+K)
4. Keyboard shortcuts

PART 2 · TUTORIAL

5. Build your first schedule in 12 steps

PART 3 · VIEWS

6. Gantt Chart and Tracking Gantt
7. Network, Calendar, Kanban, Timeline
8. Usage views and the Task Sheet
9. Resource views and Team Planner
10. Panes: Timeline, Details, Inspector

PART 4 · SCHEDULING

11. Tasks
12. Dependencies
13. Calendars and working time
14. Constraints, deadlines, splits, recurring tasks

PART 5 · RESOURCES AND COSTS

15. Resources and assignments
16. Costs and budgets
17. Resource leveling

PART 6 · TRACKING

18. Baselines
19. Recording progress
20. Earned value, progress lines, task path

PART 7 · CUSTOMISING

21. Tables, filters, groups and sorting
22. Custom fields and formulas
23. Formatting the Gantt chart
24. Saved views and the Organizer

PART 8 · OUTPUT AND FILES

25. Reports and Compare Projects
26. Printing, PDF and images
27. Opening, importing and exporting
28. Multiple projects and resource pools
29. Macros
30. Options, autosave and recovery

APPENDIX

A. Typing durations, dates and links
B. Troubleshooting
C. About Planora

PART 1 · GETTING STARTED

1. Installing Planora

Planora installs with a single Setup file and needs nothing else on the PC.

System requirements

Item	Requirement
Operating system	Windows 10 or Windows 11, 64-bit
Disk space	About 300 MB
Other software	None. Planora carries everything it needs, including its own copy of .NET.
Administrator rights	Not needed. Planora installs for the current Windows user.
Internet	Not needed, for installing or for using Planora.

Install

1. Copy **Planora-Setup-1.0.0.exe** to the PC and double-click it.
2. If Windows shows *"Windows protected your PC"*, click **More info** and then **Run anyway**. The Setup file is not digitally signed, so Windows does not recognise its publisher yet.
3. Check the install folder (normally `%LOCALAPPDATA%\Programs\Planora`) and the three options: *Create a desktop shortcut*, *Open .planora files with Planora*, and *Start Planora when Setup finishes*.
4. Click **Install**, wait for the files to copy, then click **Finish**.


Update or uninstall

To install a newer version, run its Setup file: it replaces the old program and keeps your project files. To remove Planora, open **Settings › Apps › Installed apps**, find **Planora** (publisher: Adeeb) and choose **Uninstall**. Your project files are never deleted.

PART 1 · GETTING STARTED

2. The Planora window

The schedule is the centre of the screen. Everything else sits around it.

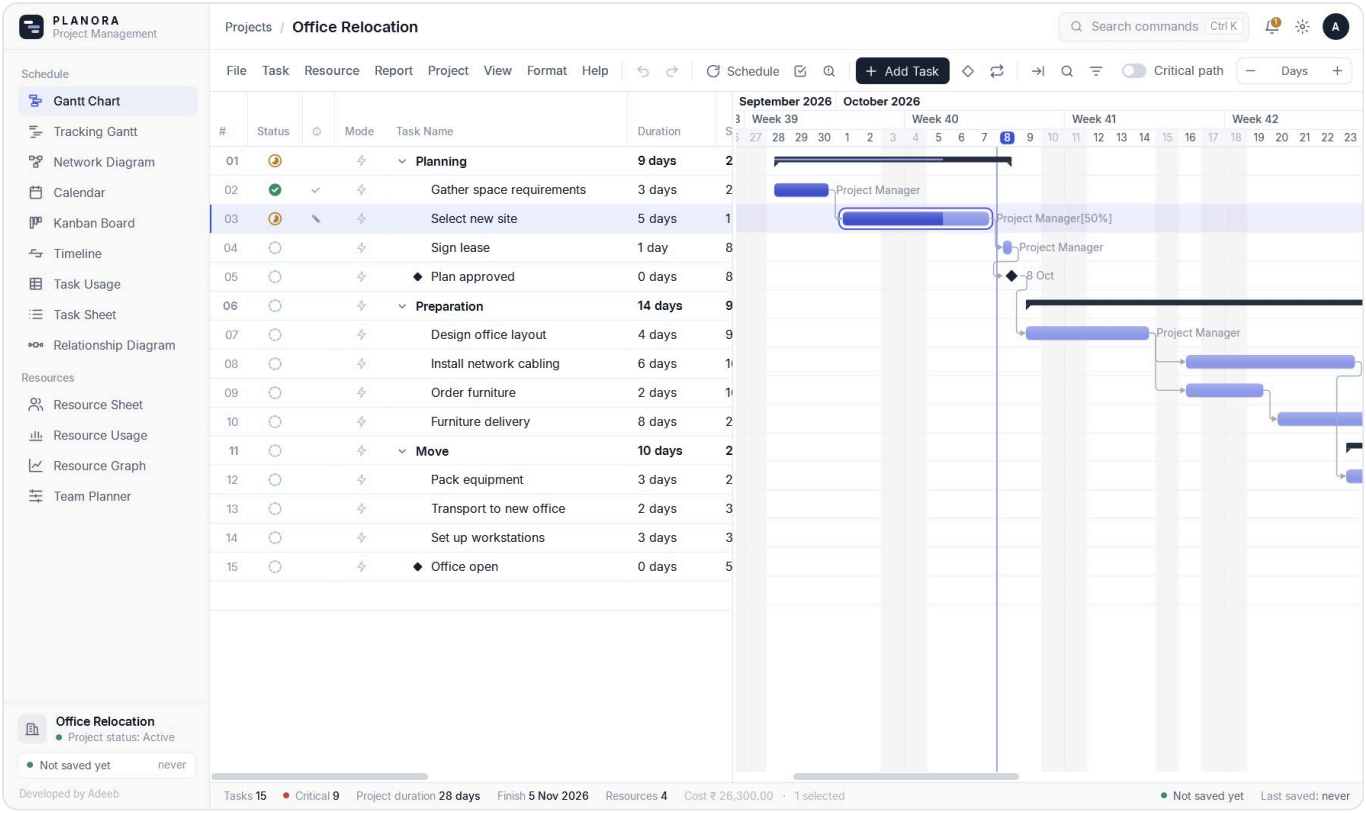

The Gantt Chart view with the sample project open and task 3 selected.

Area	What it does
Sidebar (left)	Switches between views, grouped into **Schedule** and **Resources**. The selected view is tinted with an accent mark. At the bottom: the project name and status (Not started, Active or Complete), whether your changes are saved, and when you last saved.
Top bar	The breadcrumb shows the folder and project name; a **Baseline** chip appears once a baseline is saved and an **Edited** chip while there are unsaved changes. On the right: **Search commands** (Ctrl+K), the **bell** with schedule warnings, **Options**, and the account menu (accent colour, About).
Command bar	The menus **File, Task, Resource, Report, Project, View, Format, Help** hold every command. Next to them are the everyday commands: Undo, Redo, Schedule, Update Tasks, Inspect, **Add Task**, Milestone, Recurring Task, Go To Task, Find, Filter and Task Properties. On the right: the **Critical path** switch and zoom.
Task table	One row per task: row number, status, indicators, scheduling mode, name and the columns of the current table. Phases (summary tasks) are bold and can be collapsed with their arrow.
Gantt chart	Bars on a timescale of months, weeks and days, with today marked. Hover a bar for a details card; drag it to change the schedule.

Status bar	Number of tasks, critical tasks, project duration, finish date, resources, the latest message, and the save state.

The status marks


Mark	Meaning
Green tick	Complete (100%).
Indigo ring	In progress; the ring fills with the percentage complete.
Amber ring	Behind schedule at the status date (or today).
Dashed ring	Not started.

In the **Mode** column a lightning icon means *auto scheduled* (Planora calculates the dates) and a pin means *manually scheduled* (you fix the dates).

PART 1 · GETTING STARTED

3. Command search (Ctrl+K)


You never need to remember where a command lives. Press `Ctrl` + `K` or click **Search commands** and type a few letters.

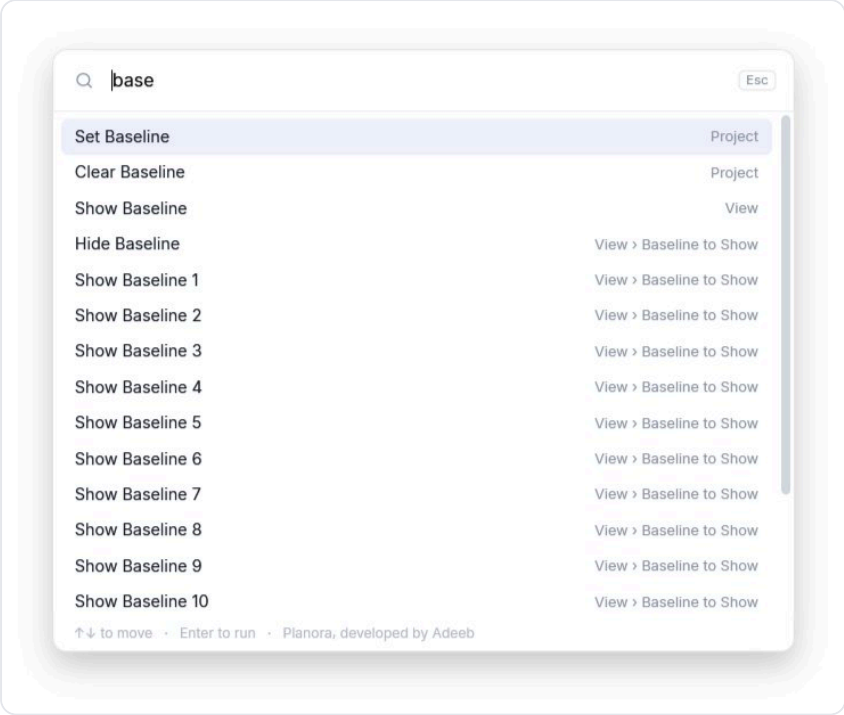

Typing “base” finds every baseline command.

The search covers every menu command, every view, every table, filter and group, and every task in the project. Use `↑` `↓` to move and `Enter` to run; choosing a task selects it and scrolls the chart to it. `Esc` closes the search.

The menus

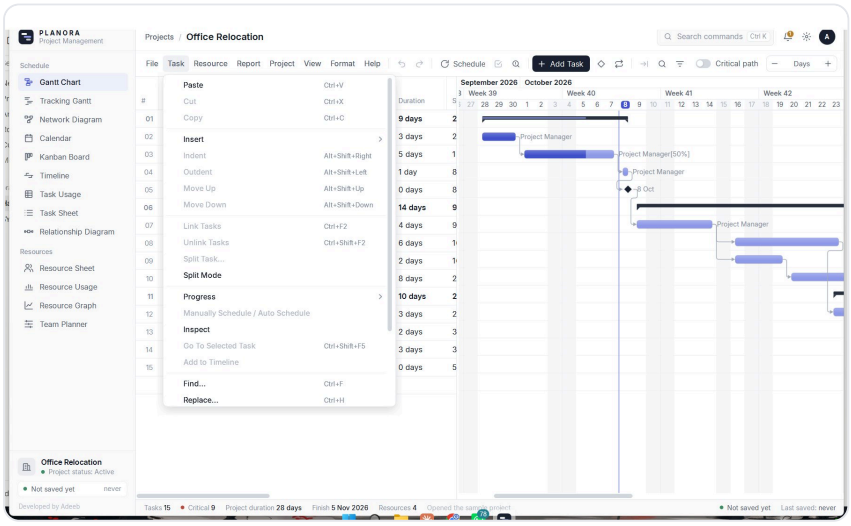

The Task menu, with keyboard shortcuts on the right.

Menu	Contains

File	Opens the File page: Info, New, Open (with recent projects), Save, Save As, Print (with preview), Export, Options and About.
Task	Clipboard, Insert (task, summary, milestone, recurring task), indent and outdent, move up and down, link and unlink, split, progress (0–100%, Mark on Track, Update Tasks), scheduling mode, Inspect, Go To, Add to Timeline, Find, Replace, Fill Down, Spelling, Task Information, hyperlinks and Delete.
Resource	Resource views, Resource Information, Delete Resource, Budgets, resource pool commands and Level Resources.
Report	Dashboards, task and resource reports, the report designer, Compare Projects, PDF, image, Print and Page Setup.
Project	Project Information, Custom Fields, Change Working Time, Calculate Project, baselines, Update Project, links to other projects, subprojects, Import and Export.
View	Table, Filter, Group, Sort, Define (tables, filters, groups, fields, Organizer), Expand/Collapse All, zoom, critical path, baselines, progress lines, usage details, Timeline and Details panes, saved views and Macros.
Format	Text Styles, Bar Styles, Gridlines, Timescale, Task Path, Columns and Custom Fields.
Help	Search Commands, Open Sample Project and About Planora.

4. Keyboard shortcuts

Keys	Command
`Ctrl` + `K`	Search commands and tasks
`Ctrl` + `N`	New project
`Ctrl` + `O`	Open
`Ctrl` + `S`	Save
`F12`	Save As
`Ctrl` + `P`	Print
`Ctrl` + `Z`	Undo
`Ctrl` + `Y`	Redo
`Insert`	Insert task
`Delete`	Delete selected tasks
`Ctrl` + `C` / `X` / `V`	Copy, cut, paste tasks
`Ctrl` + `D`	Fill down

Keys	Command
`Alt` + `Shift` + `→` / `←`	Indent / outdent
`Alt` + `Shift` + `↑` / `↓`	Move task up / down
`Ctrl` + `F2`	Link selected tasks
`Ctrl` + `Shift` + `F2`	Unlink tasks
`Shift` + `F2`	Task Information
`Ctrl` + `Shift` + `F5`	Scroll to the selected task
`F9`	Recalculate the schedule
`Ctrl` + `F` / `Ctrl` + `H`	Find / Replace
`F7`	Spelling
`Alt` + `F8`	Macros
`Ctrl` + `+` / `Ctrl` + `−`	Zoom in / out
`Ctrl` +mouse wheel	Zoom around the mouse
`Shift` +mouse wheel	Scroll the chart sideways

Mouse actions in the Gantt chart

Action	Result
Drag the middle of a bar sideways	Moves the task. An auto-scheduled task gets a *Start No Earlier Than* constraint on the new date; a manual task simply moves.
Drag the right edge of a bar	Changes the duration.
Drag the left edge of a bar	Sets the percentage complete.
Drag a bar up or down onto another task	Links the two tasks (finish-to-start).
Double-click a bar	Opens Task Information.
Hover a bar	Shows duration, start, finish, progress, deadline and slack.
Right-click a column header	AutoFilter: show only rows with chosen values in that column.

Every change, whether typed, dragged or made in a dialog, can be undone with `Ctrl` + `Z`.


PART 2 · TUTORIAL

5. Build your first schedule in 12 steps

This tutorial builds a small construction schedule from scratch, then tracks and reports it. Allow about 20 minutes.

Step 1 · Create the project


1. Open **File › New** and choose **Blank project**. (To practise on a finished plan instead, choose **Sample project**.)
2. Open **Project › Project Information**. Enter the project name, set the **Start date** (for example Monday 4 January 2027) and leave *Schedule from* as **Project start date**. Click OK.

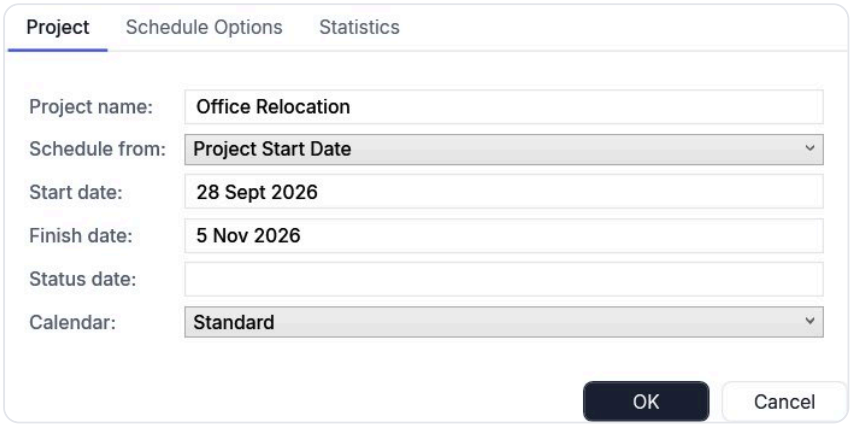

Project Information: start or finish date, status date, calendar and scheduling options.

Step 2 · Set the working time

1. Open **Project › Change Working Time**.
2. On the **Exceptions** tab add public holidays and site shutdowns. On the **Work Weeks** tab change the working days and hours (for example a six-day site week) for all or part of the project.

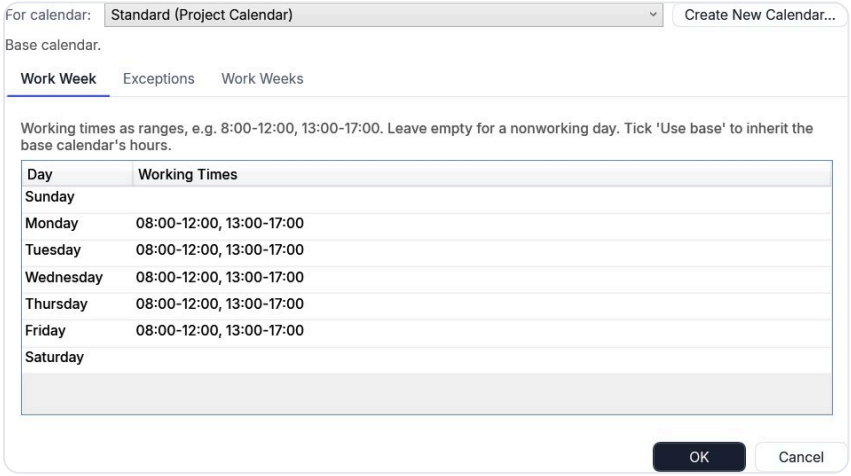

Change Working Time: calendars, exceptions and work weeks.

Step 3 · Enter the tasks

1. Click the empty row at the bottom of the task table, type a task name and press `Enter`. Repeat for each task. Or click **Add Task** (or press `Insert`) to insert above the selected row.
2. Type durations in the **Duration** column: `5d` for five working days, `2w` for two weeks, `4h` for four hours. Add `?` for an estimate (`3d?`).

> **Tip.** New tasks are auto-scheduled: Planora calculates their dates from links and the calendar. To make new tasks manually scheduled instead, use **File › Options**.

Step 4 · Organise phases


1. Insert a task named after the phase (e.g. *Foundation*) above its tasks.
2. Select the tasks under it and press `Alt` + `Shift` + `→` (**Task › Indent**). The phase becomes a bold summary task whose dates and progress roll up from its tasks.
3. Click the arrow next to a phase to collapse or expand it, or use **View › Collapse All / Expand All**.

Step 5 · Add milestones

Select the row where the milestone belongs and click **Milestone** in the command bar. A milestone has zero duration and shows as a diamond. Any task can also be shown as a milestone from Task Information.

Step 6 · Link the tasks

1. Select two or more tasks in order (hold `Ctrl` to pick several) and press `Ctrl` + `F2`. Each is linked finish-to-start to the next.
2. For other link types, type in the **Predecessors** column: `3` (finish-to-start after row 3), `3SS+2d` (start two days after row 3 starts), `5FF`, `7FS-1d` (one day of lead), `4FS+50%`.
3. Or drag a bar up or down onto the task it should come before.

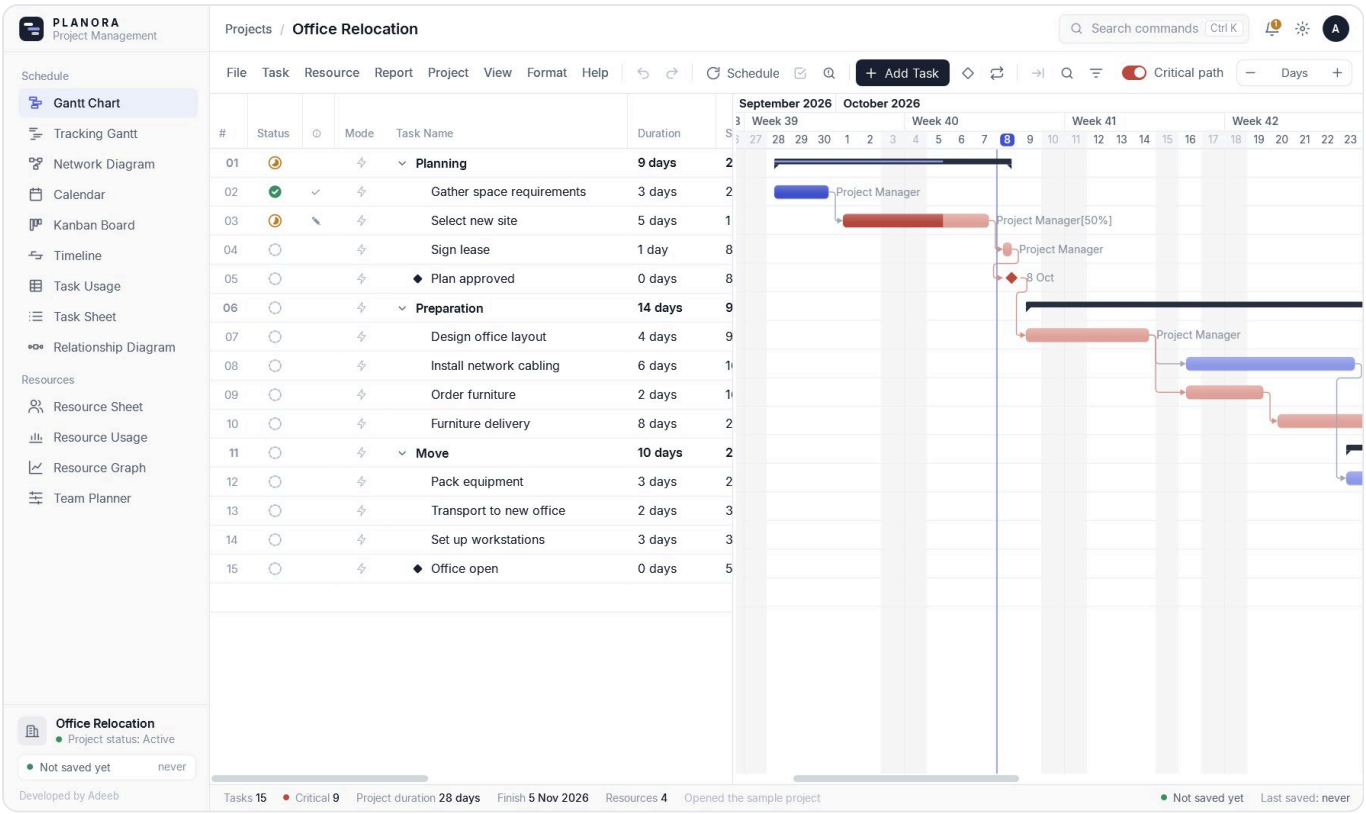


A linked schedule with the Critical path switch on: critical tasks and their links turn red.

PART 2 · TUTORIAL

Step 7 · Add resources


1. Click **Resource Sheet** in the sidebar.
2. Type one resource per row. Set the **Type**: *Work* for people and equipment paid by time, *Material* for consumables (with a **Material Label** such as m³ or crates), *Cost* for fixed charges such as permits.
3. Fill in **Max. Units** (100% is one full-time person; 300% is a crew of three), **Std. Rate**, **Ovt. Rate** and **Cost/Use**.

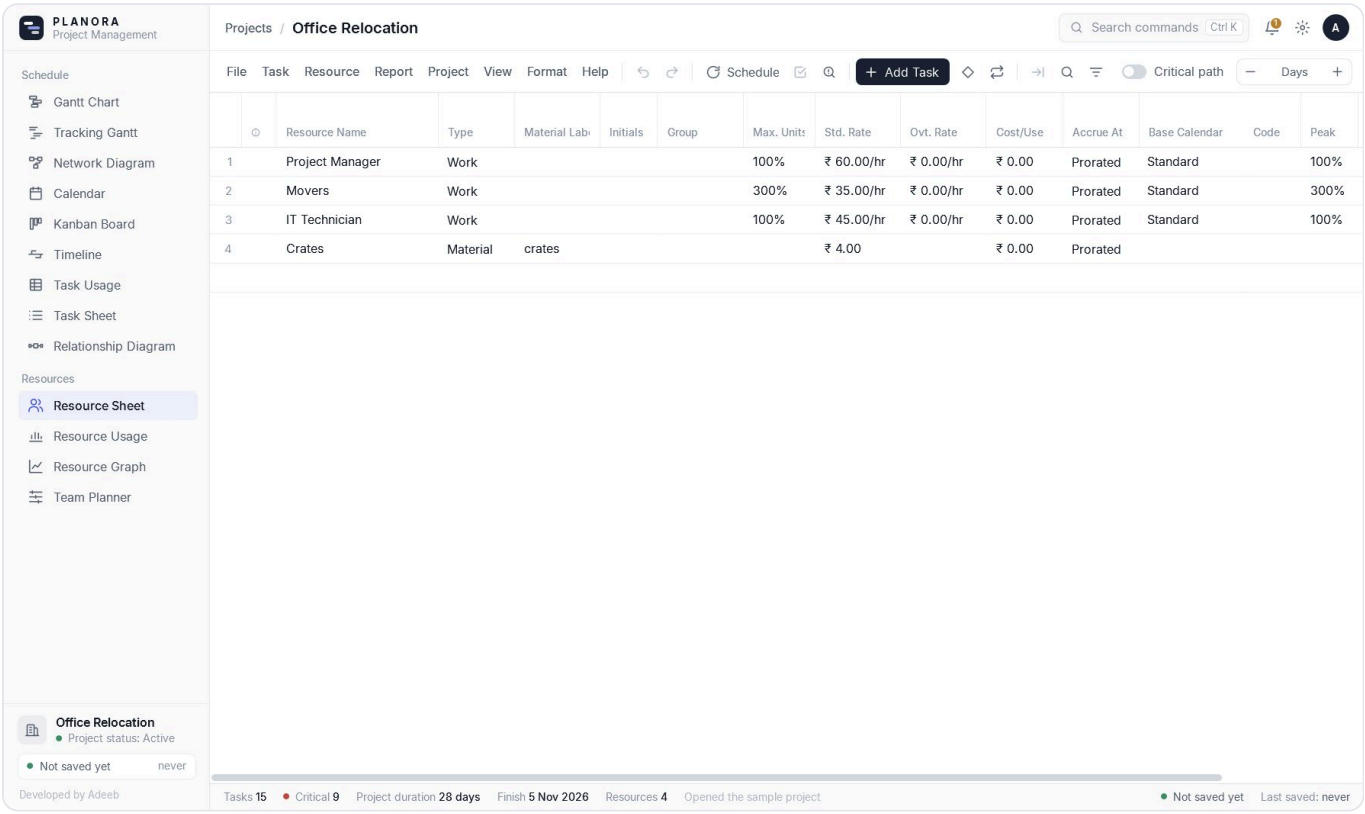

The Resource Sheet.

Step 8 · Assign resources to tasks

1. Return to the Gantt Chart. In the **Resource Names** column type names separated by commas, optionally with units: `Movers[200%], Crates[40]`.
2. Or open **Task Information** (`Shift` + `F2`) and use its **Resources** tab, where you can also set units and work per assignment.

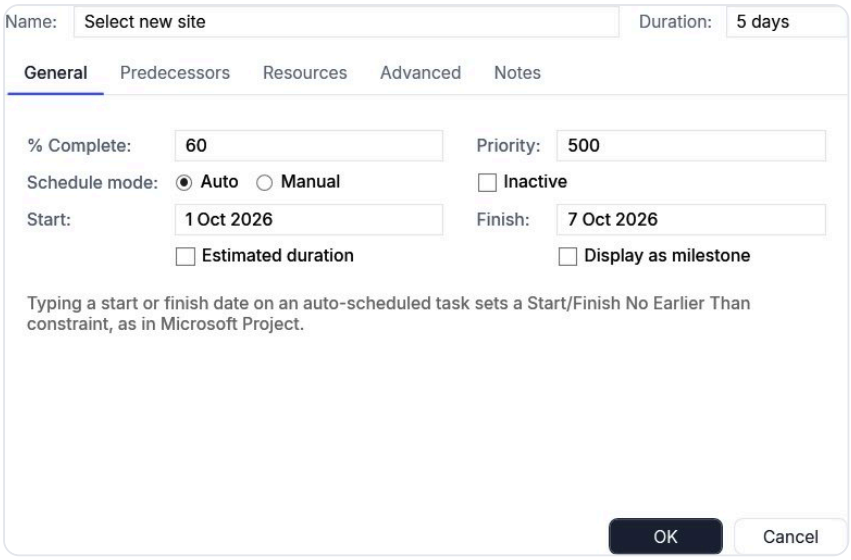

Task Information: General, Predecessors, Resources, Advanced and Notes tabs.

Step 9 · Check the schedule

- Turn on **Critical path** in the command bar to see the chain of tasks that sets the finish date.
- Click the **bell** for warnings: late tasks, missed deadlines and overallocated resources.
- Select a task and click **Inspect** to see exactly what drives its start (a predecessor, a constraint, the calendar).
- If a resource is overallocated, open **Resource › Level Resources** (chapter 17).

Step 10 · Save a baseline

When the plan is approved, open **Project › Set Baseline**, choose **Baseline** and **Entire project**, and click OK. Planora stores the planned dates, durations, work and costs so you can compare progress against them later. The top bar now shows a **Baseline** chip.

Step 11 · Track progress

1. Set the status date in **Project › Project Information** (or leave it empty to use today).
2. Select tasks and use **Task › Progress** (0, 25, 50, 75, 100%), drag the left edge of a bar, or open **Update Tasks** to enter actual start, actual finish, actual and remaining duration.
3. Switch to **Tracking Gantt** to see current bars over the grey baseline bars, or turn on **View › Progress Lines**.

Step 12 · Report and share

1. Open a report from the **Report** menu (for example *Project Overview* or *Critical Tasks*).
2. Save the current view or a report as PDF from **Report › Export as PDF**, or print it with `Ctrl` + `P`.
3. Save the project with `Ctrl` + `S` (.planora). To send it to a Microsoft Project user, use **Project › Export** and choose **Microsoft Project XML**.

Done. You have built, linked, resourced, baselined, tracked and reported a schedule. The rest of this manual describes each feature in detail.

PART 3 · VIEWS

6. Gantt Chart and Tracking Gantt


The main working view: the task table on the left and the timeline on the right, scrolled together.

Gantt bars

Bar	Meaning
Indigo bar	An auto-scheduled task. The darker part inside is the work completed.
Red bar	A critical task (only while the Critical path switch is on).
Teal bar	A manually scheduled task.
Dashed outline	An inactive task (kept for reference; it no longer affects the schedule).
Thin navy bar with end points	A summary task (phase).
Diamond	A milestone.
Dotted gap between bar pieces	A split task (work interrupted and resumed).
Green/red down arrow	A deadline: green when met, red when missed.
Grey bar underneath	The baseline (Tracking Gantt, or **View › Baseline**).

Text beside bars (resource names by default) and every colour and shape can be changed in **Format › Bar Styles**. The timescale shows month, week and day at day zoom; zoom out for weeks, months, quarters and years, or in for hours.

Tracking Gantt

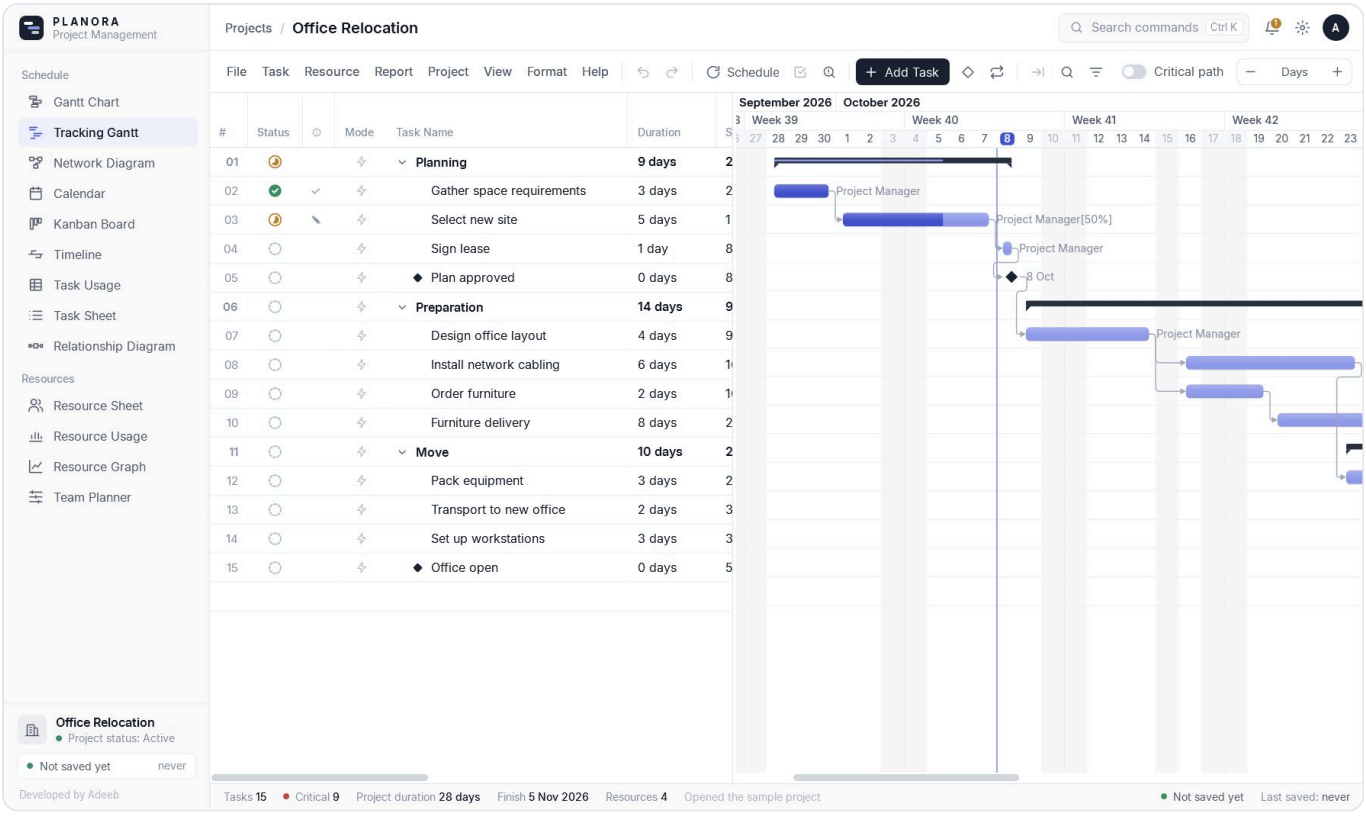

Tracking Gantt: current bars with the baseline drawn underneath.


Choose which of the 11 baselines to show in **View › Baseline to Show**.

PART 3 · VIEWS

7. Network, Calendar, Kanban and Timeline

Network Diagram


Each task is a box with its dates, duration, ID and resources; arrows show the links. Completed tasks are shaded green, in-progress tasks crossed, critical tasks outlined in red when the critical path is on.

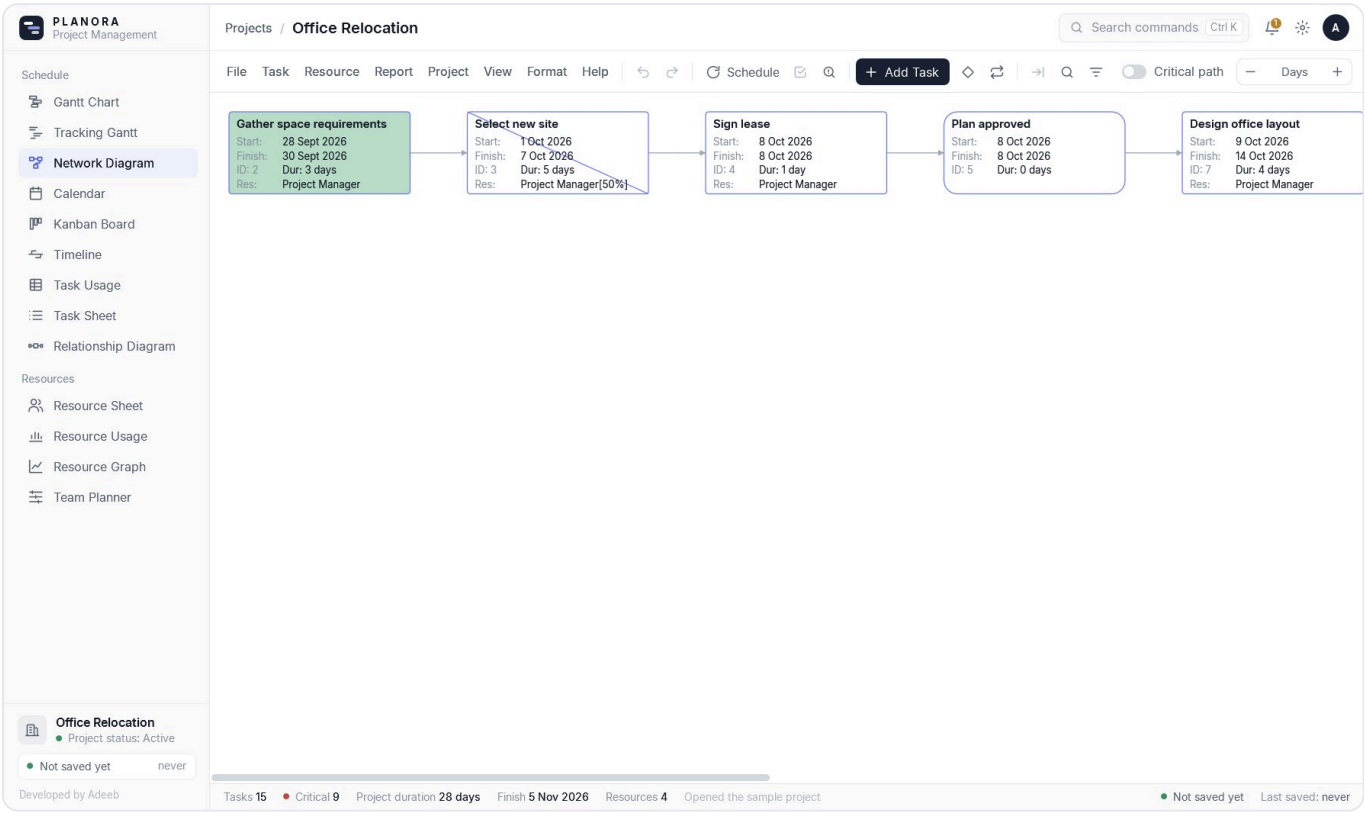

Network Diagram.

Calendar

A month calendar with task bars across the days they run, for a quick “what happens this month” view.

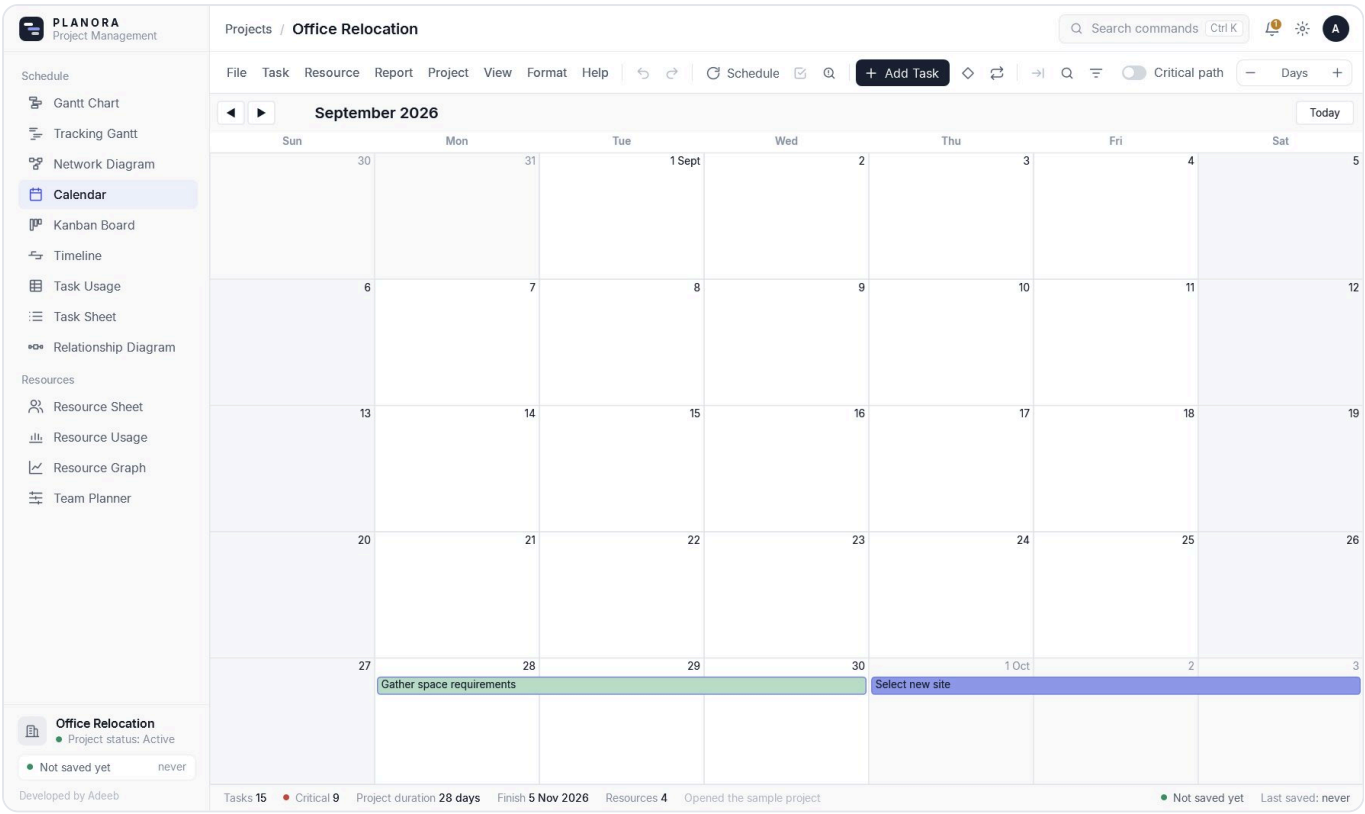


Calendar view.

PART 3 · VIEWS

Kanban Board


Tasks as cards in **Not Started**, **In Progress** and **Complete** columns, with dates, resources and a progress bar. Drag a card to another column to update its progress.

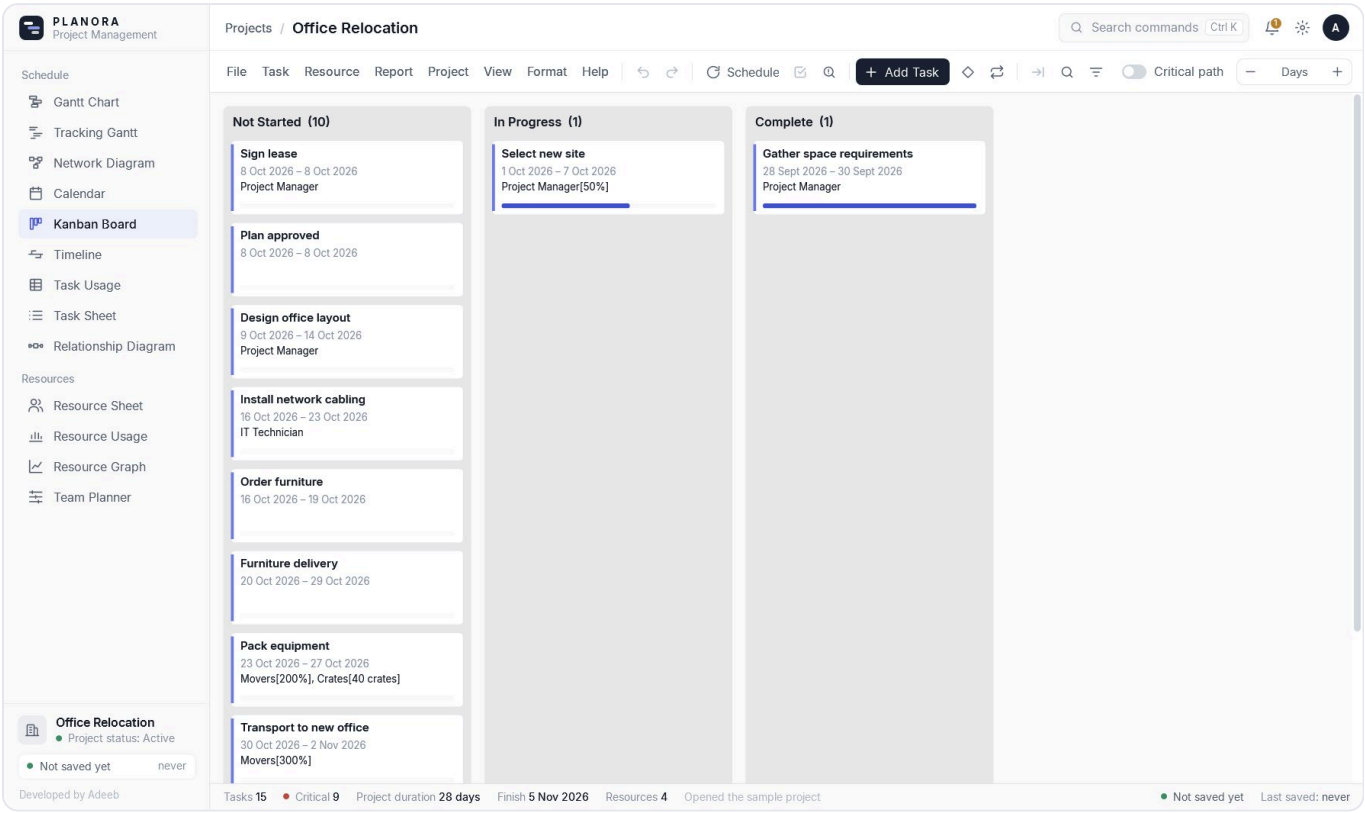

Kanban Board.

Timeline

A one-page summary of key tasks and milestones for presentations. Add tasks with **Task › Add to Timeline**. The Timeline can also be shown above any view (**View › Timeline Pane**).

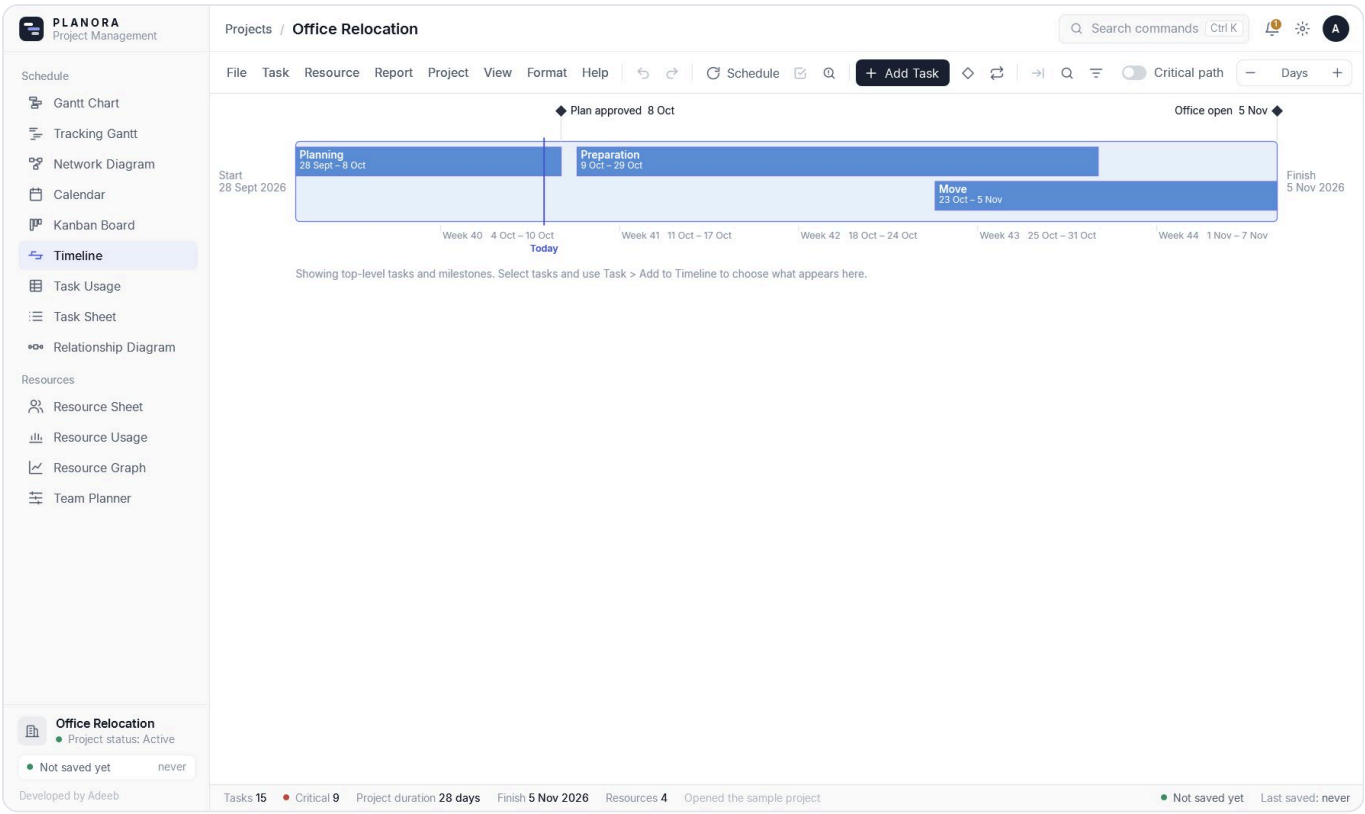


Timeline view.

PART 3 · VIEWS

8. Usage views, Task Sheet and Relationship Diagram

Task Usage

Each task with its assignments underneath, and work spread across the timescale. Choose the detail rows (work, actual work, remaining work, baseline work, cost, actual cost, baseline cost) in **View › Usage Details**.

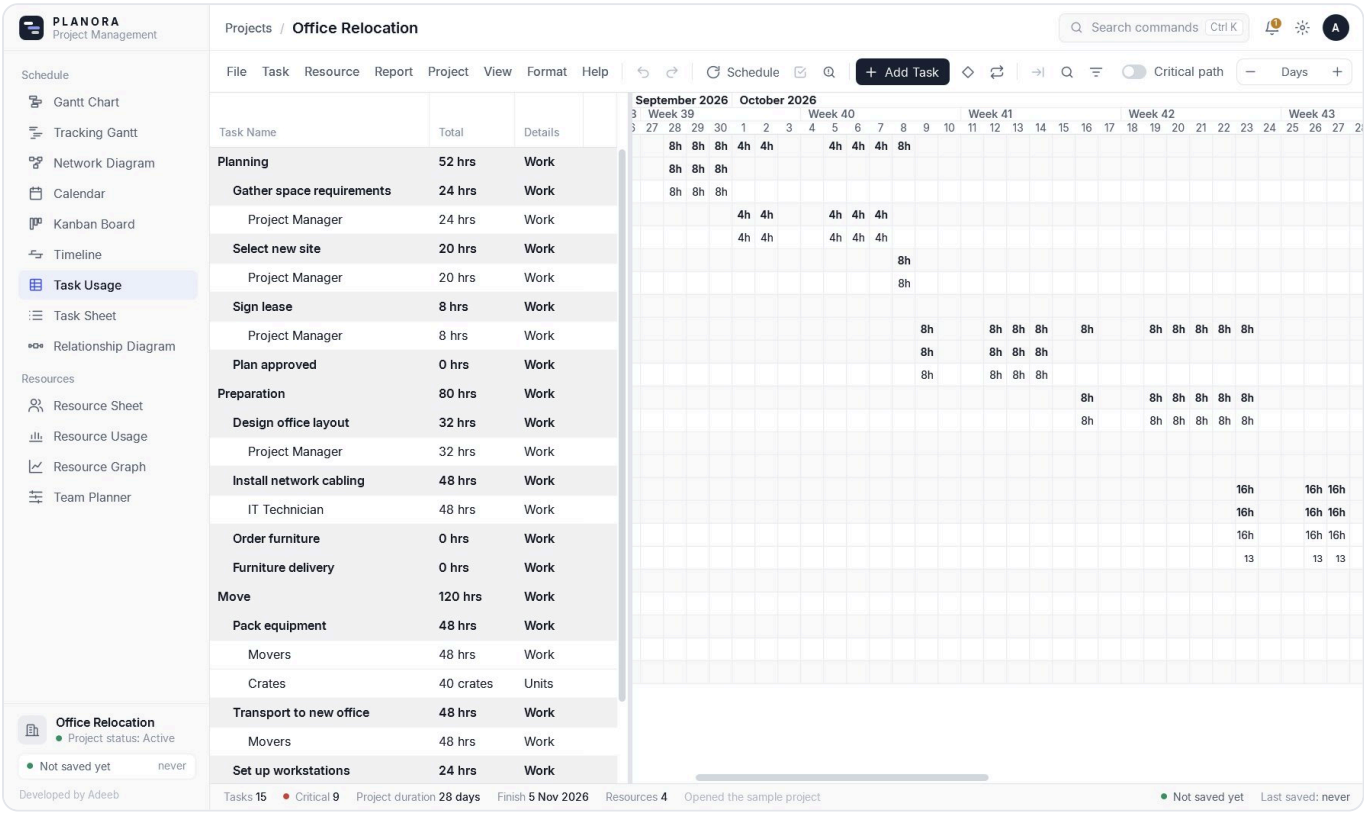

Task Usage.

Task Sheet

The task table on its own, full width, for data entry and long tables.

Relationship Diagram


The selected task in the middle with its direct predecessors on the left and successors on the right: a quick way to check one task's links.

PART 3 · VIEWS

9. Resource views and Team Planner

Resource Usage


Each resource with the tasks assigned to it and work per period. Overallocated resources and periods are shown in red.

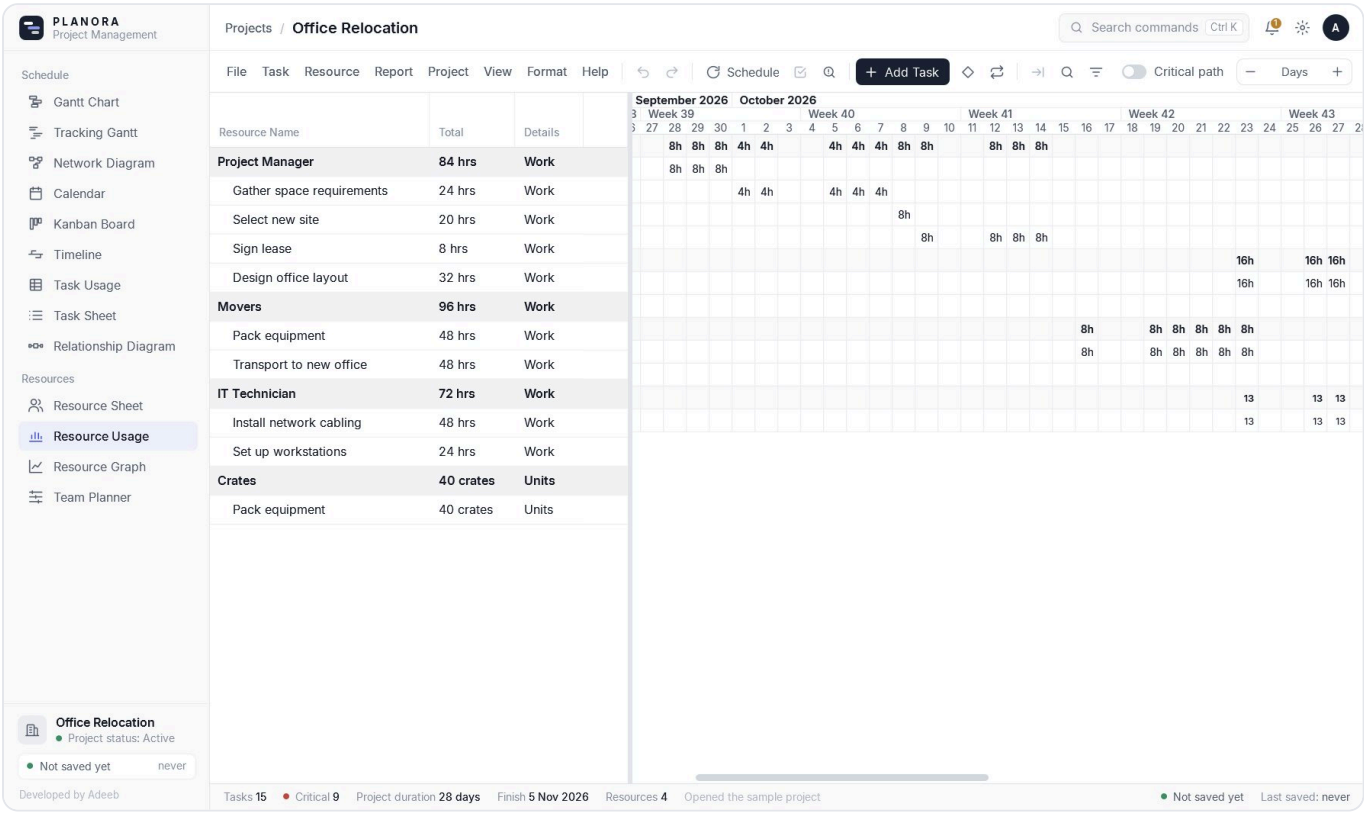

Resource Usage.

Resource Graph

A histogram of the selected resource's allocation against its maximum units, period by period; bars above the line are overallocation.

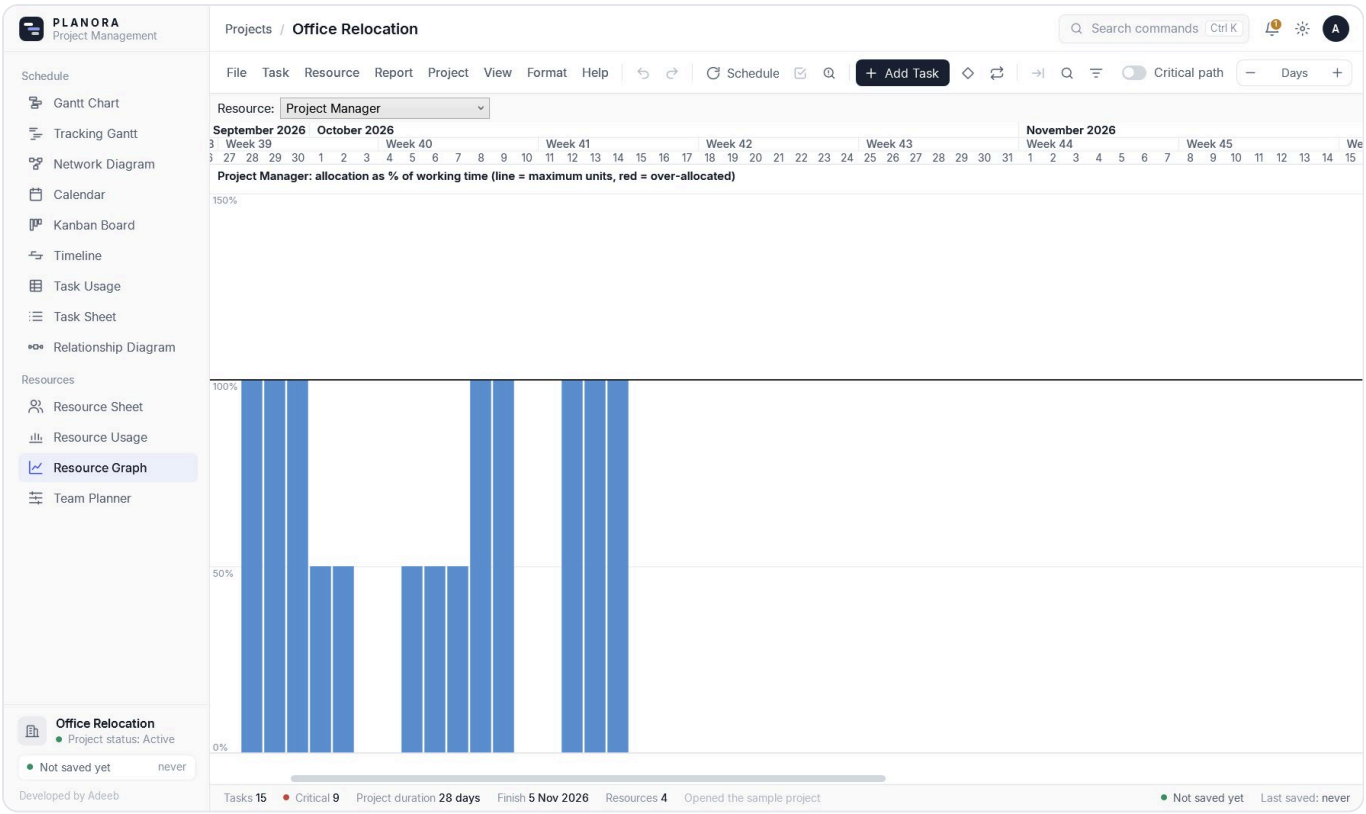


Resource Graph.

PART 3 · VIEWS

Team Planner


One row per resource with its tasks as blocks over time, plus a row of **unassigned tasks**. Drag a block to another resource's row to reassign it, or along the row to reschedule it.

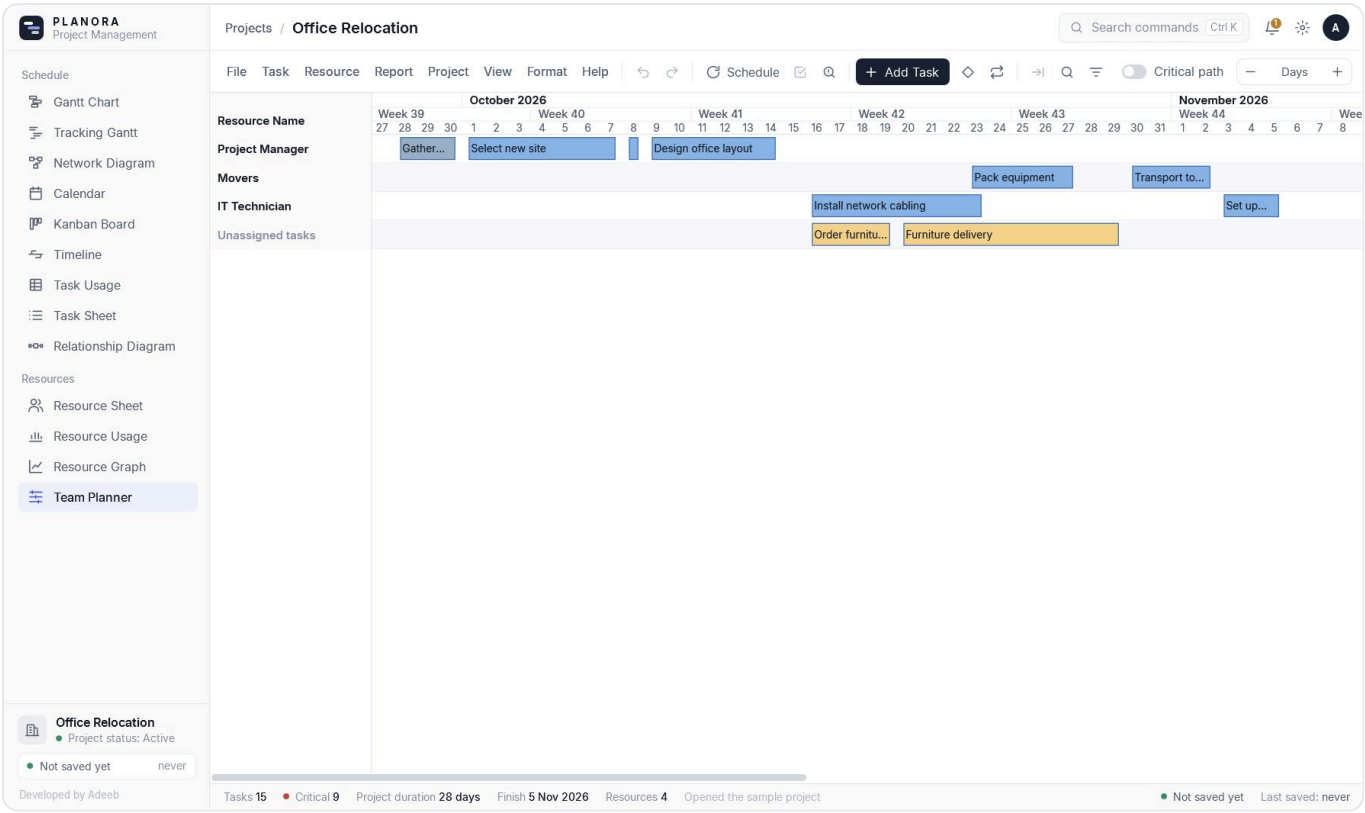


Team Planner.

10. Panes: Timeline, Details and Task Inspector


- **Timeline pane** (**View › Timeline Pane**): the Timeline above the current view.
- **Details pane** (**View › Details Pane**): the Task Form under task views (name, dates, duration, % complete, assignments, predecessors) or the Resource Form under resource views.
- **Task Inspector** (**Inspect** button): explains the selected task's start — the predecessor, constraint, calendar or actual date that sets it — and lists problems such as overallocation, with fixes.

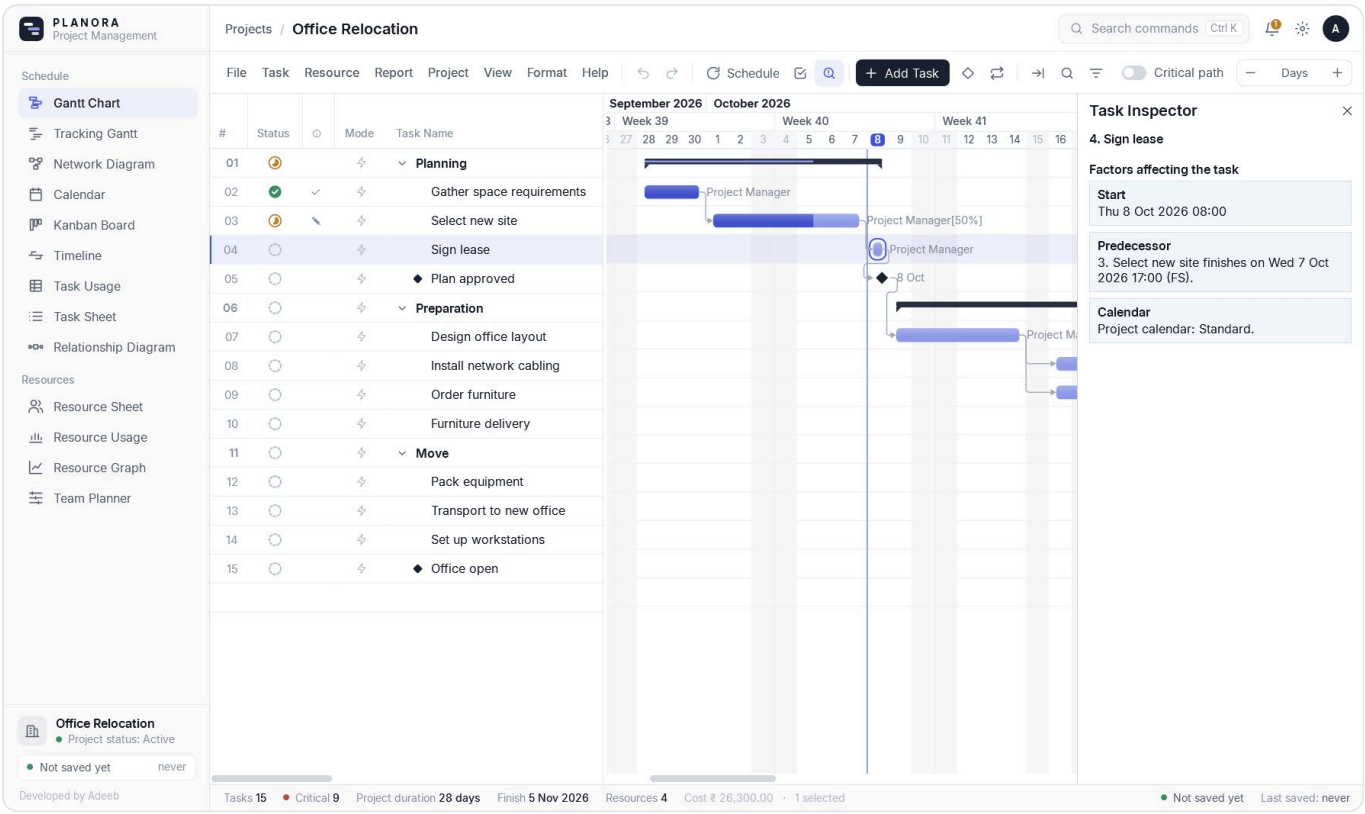

Task Inspector: “Sign lease” starts on 8 Oct because its predecessor “Select new site” finishes on 7 Oct.

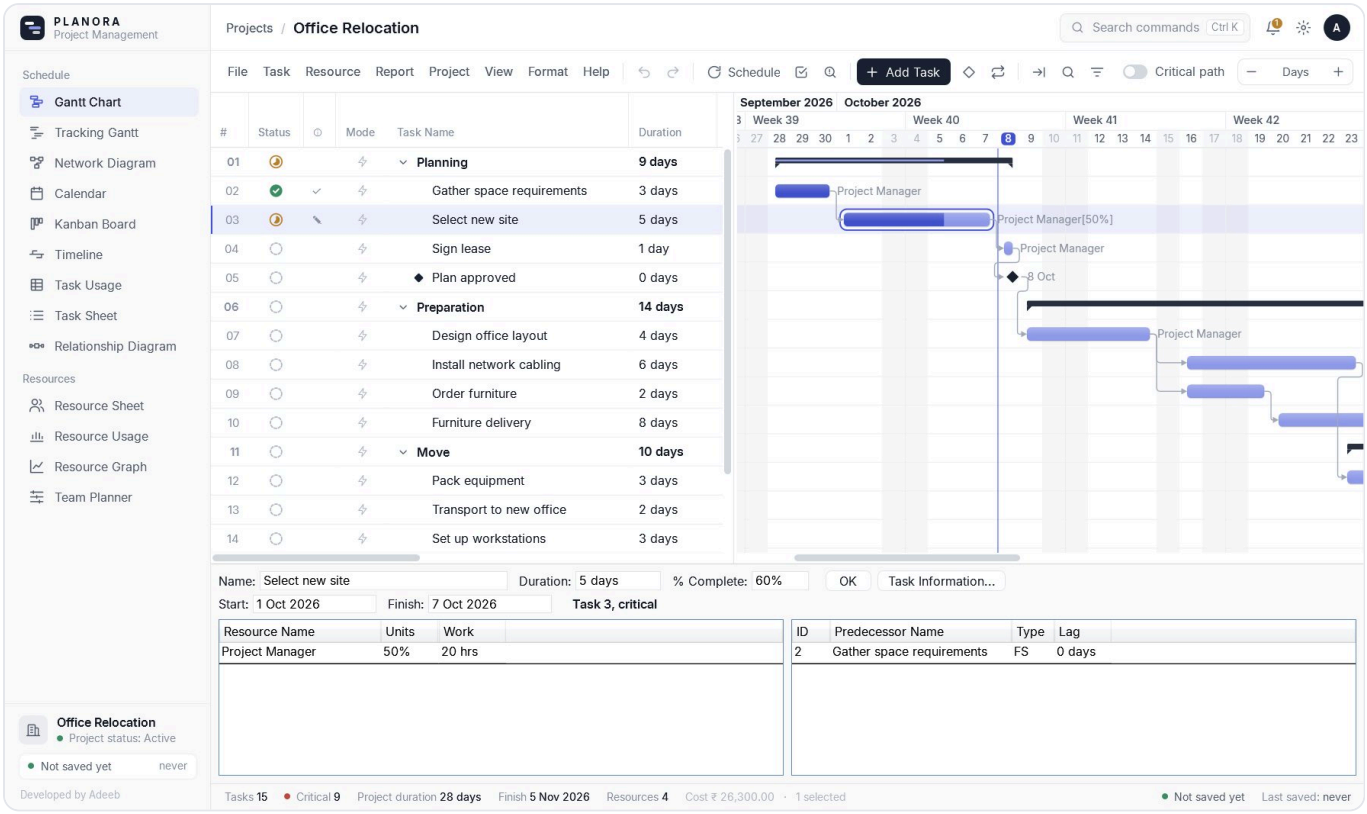

The Details pane (Task Form) under the Gantt Chart.

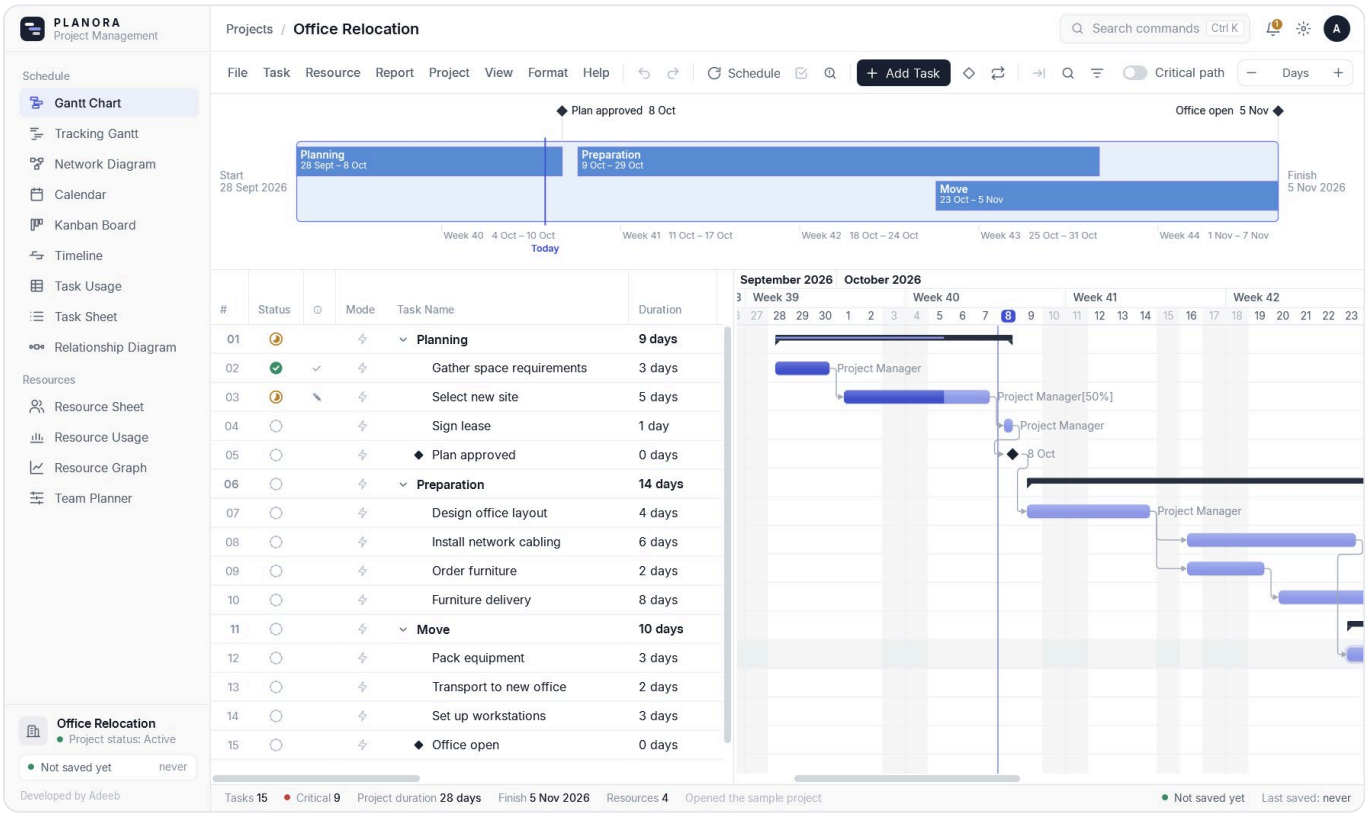

The Timeline pane above the Gantt Chart.

PART 4 · SCHEDULING

11. Tasks


Planora schedules with the critical path method: from the project start, through the links, on the working calendars, honouring constraints, actual dates and resource availability.

Task properties (Task Information)

Property	Use
Name, duration	Duration in minutes, hours, days, weeks or months; *elapsed* durations (`3ed`) run through nights and weekends; `?` marks an estimate.
Schedule mode	**Auto**: Planora calculates dates. **Manual**: you set start and finish; links are shown but do not move the task.
Task type	**Fixed Units**, **Fixed Duration** or **Fixed Work**: which of duration, units and work stays fixed when another changes. **Effort driven**: adding a resource shortens the task.
Constraint	As Soon As Possible, As Late As Possible, Must Start On, Must Finish On, Start/Finish No Earlier Than, Start/Finish No Later Than.
Deadline	A target date that does not move the task but warns when missed.
Calendar	A task calendar replaces the project calendar for that task (e.g. a 24/7 curing task).
Priority	0–1000; leveling delays lower-priority tasks first. 1000 is never delayed.
Inactive	Keeps the task but removes it from the schedule and costs (what-if planning).
Display as milestone, Mark	Show any task as a diamond; flag tasks for a filter.
Earned value method	% Complete or Physical % Complete.
Notes, hyperlink	Free text and a link to a web page or file (**Task › Open Hyperlink**).
WBS code	Calculated from the outline (1, 1.1, 1.2…).

Editing tasks in the table

- Type directly into cells; a typed start or finish date on an auto-scheduled task sets a *No Earlier Than* constraint.
- Cut, copy and paste whole tasks with `Ctrl` + `X` / `C` / `V`; **Fill Down** copies a value to the rows below.
- **Find** and **Replace** search any field; **Spelling** checks names and notes.
- Insert a **summary task** around the selection with **Task › Insert › Summary Task**.

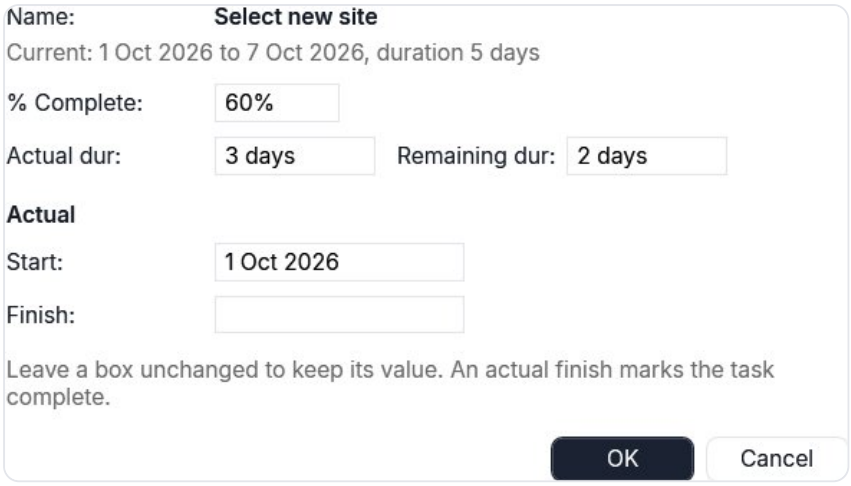

Update Tasks: percentage, actual and remaining duration, actual dates.

PART 4 · SCHEDULING

12. Dependencies

Type	Meaning	Typed as
Finish-to-start (FS)	B starts after A finishes. The most common link.	`3` or `3FS`
Start-to-start (SS)	B starts when A starts.	`3SS`
Finish-to-finish (FF)	B finishes when A finishes.	`3FF`
Start-to-finish (SF)	B finishes when A starts.	`3SF`

Lag delays the successor (`3FS+2d`); **lead** overlaps it (`3FS-1d`); lag can be a percentage of the predecessor's duration (`3SS+50%`) or elapsed (`3FS+2ed`). Several predecessors are separated by commas.


With *Autolink inserted or deleted tasks* (Project › Project Information) a task inserted into a chain is linked in automatically, and deleting one rejoins the chain. Links to tasks in **other project files** are described in chapter 28.

13. Calendars and working time


- **Base calendars**: Standard (Mon–Fri, 8:00–17:00), 24 Hours and Night Shift are provided; create your own in Change Working Time.
- **Exceptions**: holidays or special working days, one-off or recurring (daily, weekly, monthly, yearly).
- **Work weeks**: different working days and hours for a date range (e.g. summer hours).
- Calendars apply to the **project**, to individual **tasks** and to **resources**; a resource's calendar decides when its assignments can be worked.
- Hours per day, per week and days per month (for converting durations) are set in Project Information.

14. Constraints, deadlines, splits and recurring tasks

- **Constraints** fix a task to a date (see the list in chapter 11). Turn off *Honor constraints* in Project Information to let links win over constraints.
- **Deadlines** show as arrows and raise a warning when the task finishes late.
- **Split a task** with **Task › Split Task**, or switch on **Split Mode** and click a bar where the interruption should start.
- **Recurring tasks** (weekly meetings, monthly inspections) are created with **Recurring Task**: a summary with one occurrence per repetition.

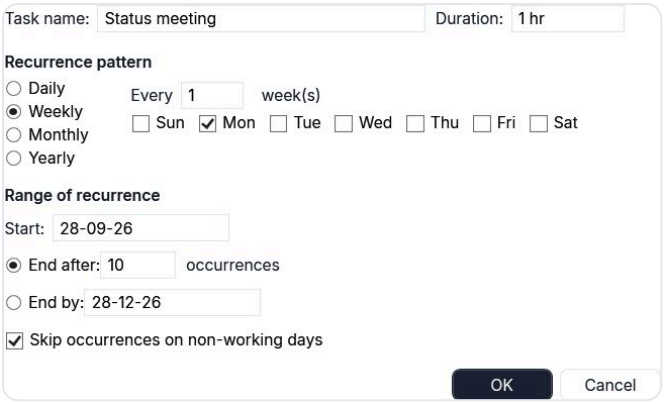


Recurring Task.

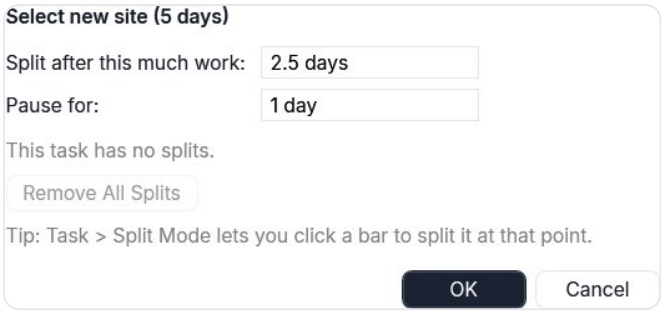

Split Task.

PART 5 · RESOURCES AND COSTS

15. Resources and assignments

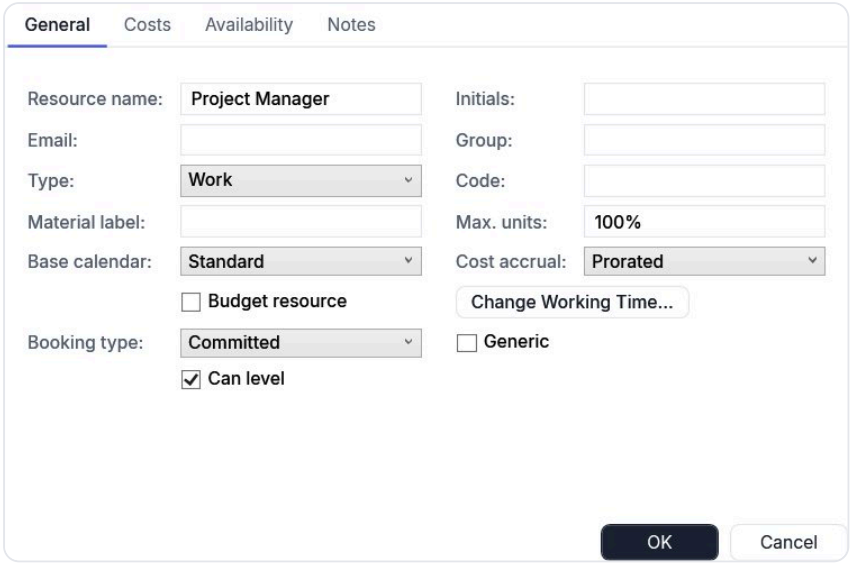

Resource Information.

Property	Use
Type	Work, Material (with a label such as m^3) or Cost.
Max units, availability	The resource's capacity, which can change over time (availability table).
Rates	Standard and overtime rates, cost per use, and up to five cost rate tables (A–E) with dated rate changes.
Accrue at	Start, Prorated or End: when the cost is counted.
Calendar	The resource's own working time and holidays.
Generic, booking type, can level	Placeholder roles, proposed or committed bookings, and whether leveling may move this resource's work.
Group, code, initials, e-mail	Information for filters, groups and reports.

Assignments

An assignment links a resource to a task with units, work and a **work contour** (flat, back loaded, front loaded, double peak, early peak, late peak, bell, turtle, or contoured period by period). Double-click an assignment in a usage view for Assignment Information: units, work, delay, cost rate table and contour.


16. Costs and budgets

- Task cost = resource costs (work × rates, per-use costs, material quantities) + **fixed cost** (Cost table).
- Actual and remaining cost follow progress; baseline cost and cost variance follow the baseline.
- **Budgets** (**Resource › Budgets**): budget cost and work for budget resources at project level, to compare against the plan.
- Costs show in your Windows currency format.

PART 5 · RESOURCES AND COSTS

17. Resource leveling

When a resource is asked to work more than its maximum units, Planora marks it as overallocated (red in resource views and a warning in the bell). **Leveling** resolves this by delaying or splitting lower-priority work.

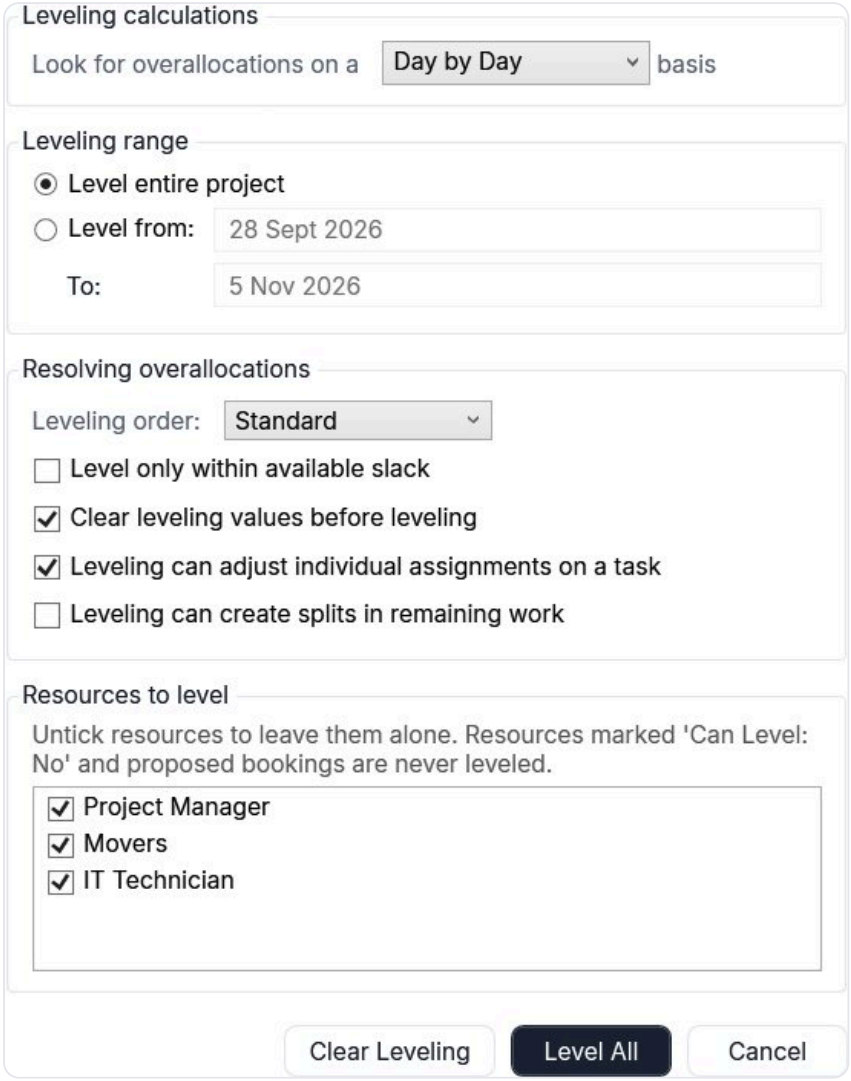


Resource Leveling.

- **Look for overallocations** minute by minute, or by hour, day, week or month.
- **Leveling range**: the entire project or a date range.
- **Leveling order**: ID only, Standard (slack, dates, priority, constraints) or Priority then Standard.
- Options: level only within available slack, clear earlier leveling first, let leveling adjust individual assignments, and let leveling split remaining work.
- **Clear Leveling** removes all leveling delays.

PART 6 · TRACKING

18. Baselines

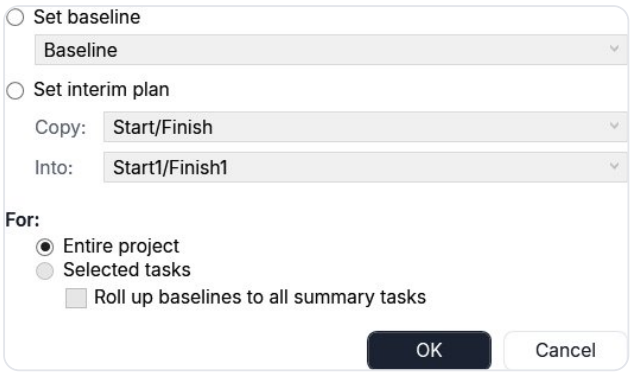

Set Baseline.


Planora keeps **11 baselines** (Baseline, Baseline 1–10) and **10 interim plans** (start and finish only). Save the whole project or only selected tasks; summary tasks can roll up the baselines of their tasks.
Project › Clear Baseline removes one. Variance fields (start, finish, duration, work, cost) compare the current plan with the baseline.

19. Recording progress

- **Status date** (Project Information): the “as of” date for progress and earned value. Empty means today.
- **% complete buttons**, dragging the bar's left edge, or typing in the % Complete column.
- **Update Tasks**: actual start and finish, actual and remaining duration.
- **Mark on Track**: records progress exactly as planned up to the status date.
- **Update Project**: marks all work complete through a date, or reschedules unfinished work to start after it.
- The **Tracking** table shows actual dates, durations, costs and work.

20. Earned value, progress lines and task path

- **Earned value**: the *Earned Value* table and report show BCWS, BCWP, ACWP, SV, CV, EAC, BAC and VAC at the status date.
- **Progress lines** (**View › Progress Lines**): a line from the status date that bends left for tasks behind and right for tasks ahead.
- **Task path** (**Format › Task Path**): highlights the selected task's predecessors, driving predecessors, successors and driven successors in different colours.

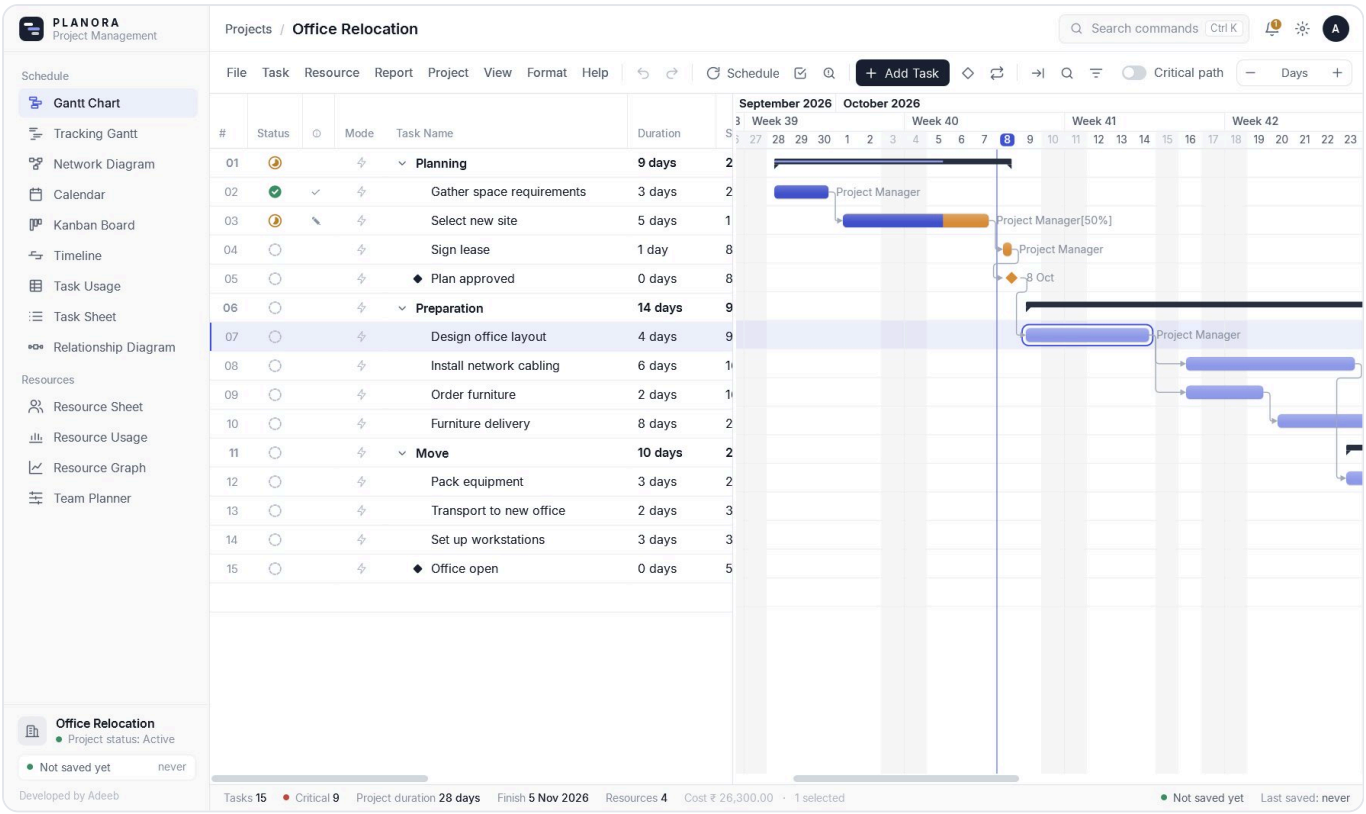

Task Path: the predecessors of the selected task highlighted.

PART 7 · CUSTOMISING


21. Tables, filters, groups and sorting

Tables

A table is the set of columns in the task table. Built in: **Entry, Schedule, Cost, Tracking, Variance, Work, Baseline, Summary, Earned Value, Constraint Dates, Delay**. Switch in **View › Table**; insert, remove and arrange columns in **Format › Columns**; create your own in **View › Define › Tables**.

Filters


Built in: All Tasks, Active, Completed, Incomplete, Critical, Late, Slipping, Milestones, Marked, Summary, Manually Scheduled, Tasks With Deadlines, Missed Deadlines, Estimated Durations and Fixed Dates. A filter can **hide** other tasks or **highlight** the matching ones. Define your own with any field and condition; a value starting with ? makes an **interactive filter** that asks for the value each time. Right-click a column header for a quick **AutoFilter**.

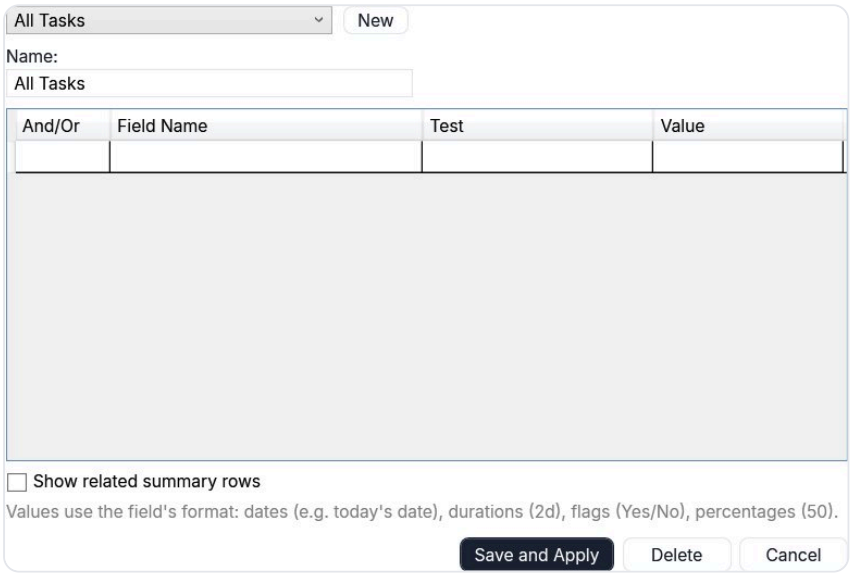

Defining a filter.

Groups and sorting

Group tasks by status, critical, milestone, duration, priority, constraint type, mode, resource or start month — or any field you choose — with roll-up bars for each group. **View › Sort** sorts by up to three fields, optionally keeping the outline.

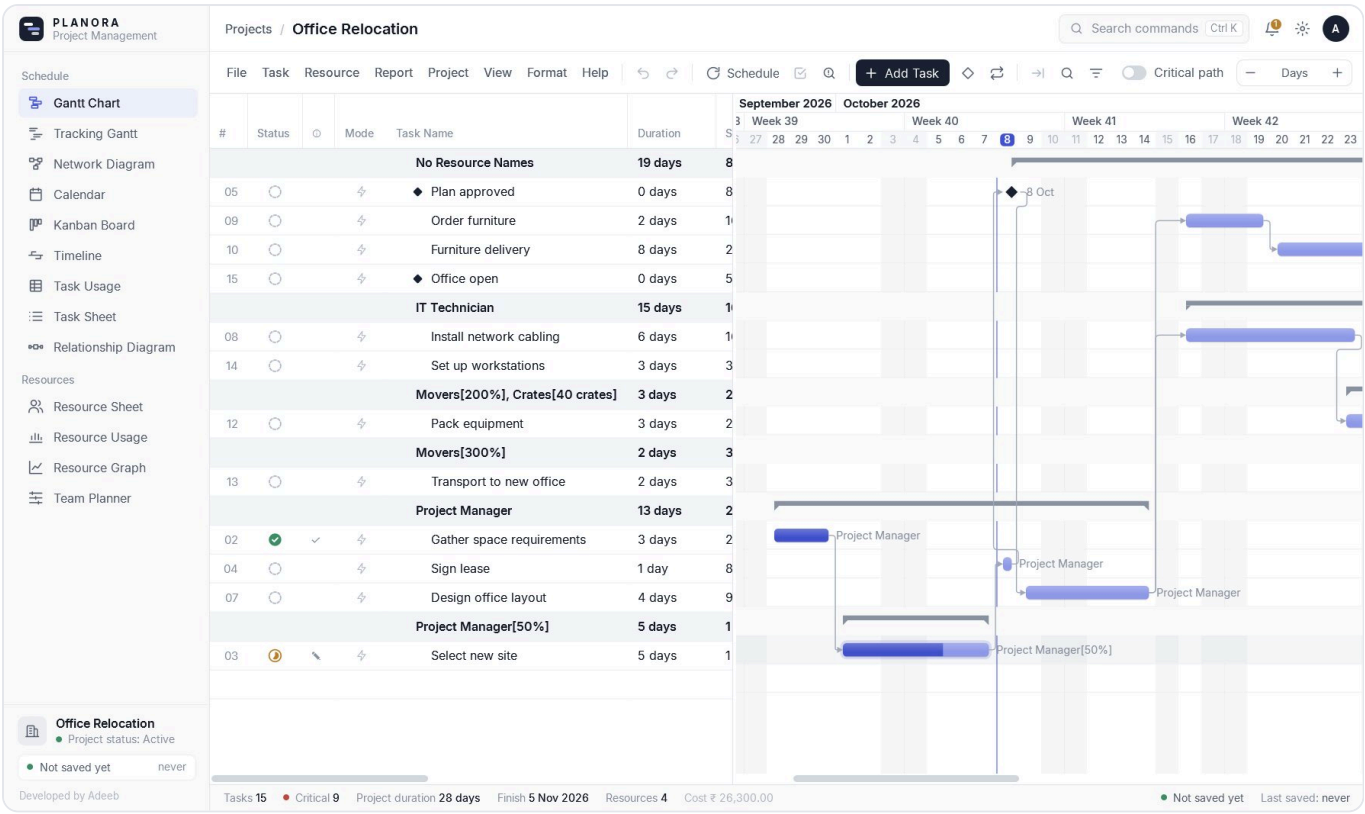


Tasks grouped by resource.

PART 7 · CUSTOMISING

22. Custom fields and formulas

Give your own meaning to the spare fields: Text 1–30, Number 1–20, Date 1–10, Flag 1–20, Cost 1–10, Duration 1–10 and Outline Code 1–10 (**Project › Custom Fields**).

- **Alias**: a name such as “Zone” or “Contractor”.
- **Lookup list**: a drop-down of allowed values.
- **Formula**: calculate from other fields, e.g. `[Cost] - [Baseline Cost]` or `IIf([% Complete] = 100, "Done", "Open")`. Functions include Iif, Switch, Abs, Round, Min, Max, Len, Left, Right, Mid, CStr, Val, Format, Now, Date, DateAdd, DateDiff and ProjDurConv.
- **Graphical indicators**: show a symbol instead of the value when conditions are met (traffic lights for variance, for example).
- **Outline codes**: hierarchical codes such as cost codes or locations, usable in groups and filters.

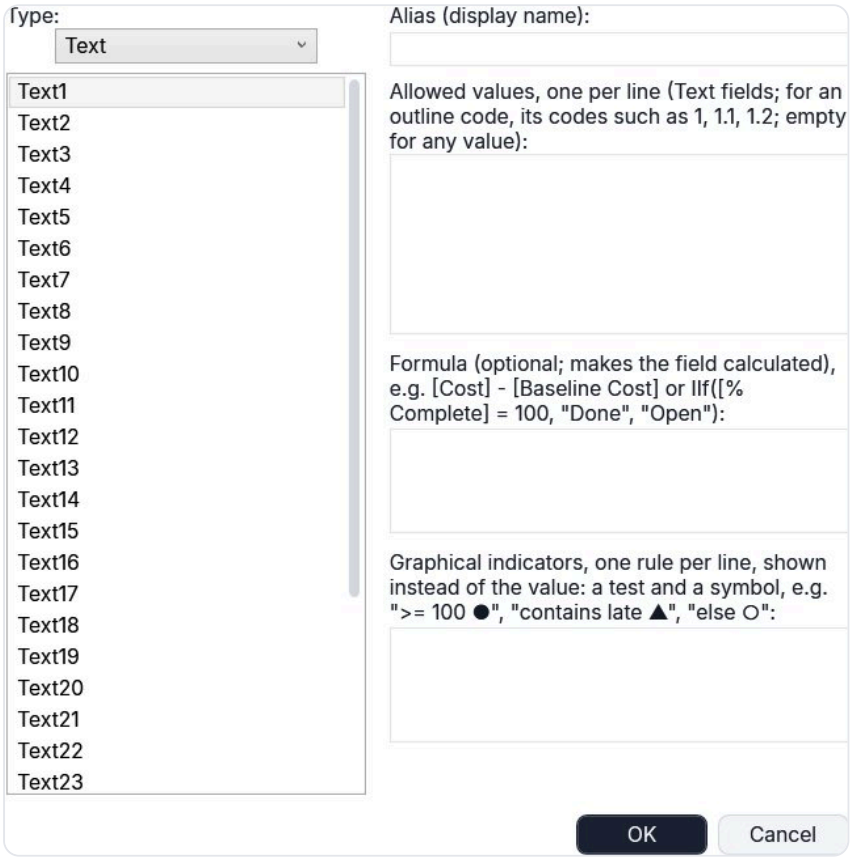


Custom Fields.

23. Formatting the Gantt chart



Bar Styles.

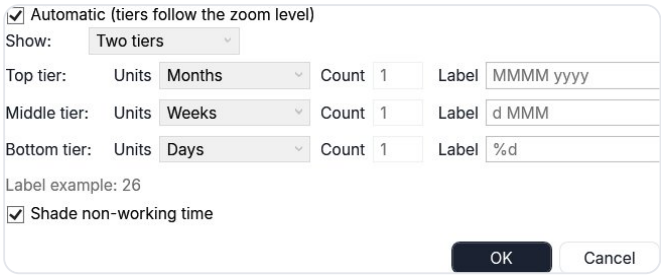


Timescale.

- **Bar Styles**: colour, border and shape of each bar type, the texts left, right, above and inside, and extra styles for tasks with a flag field set.
- **Text Styles**: font settings for bar text and for summary, critical, milestone, marked and external tasks.
- **Timescale**: one to three tiers with units (hours to years), counts and label formats; shading of non-working time.
- **Gridlines**: row and column lines, and lines for today, the status date, project start and finish.
- **Accent colour** (account menu): Indigo, Slate Blue, Teal or Graphite.

PART 7 · CUSTOMISING

24. Saved views and the Organizer

View › Save View stores the current view with its table, filter, group and sort under a name; **View › Saved Views** brings it back. The **Organizer** (**View › Define › Organizer**) copies calendars, tables, filters, groups, views, custom fields, reports and macros between projects, or deletes ones you no longer need.

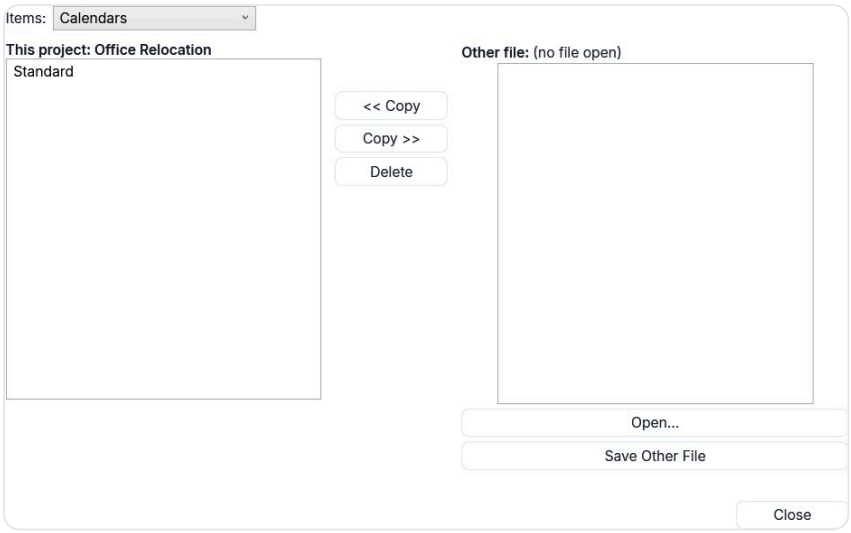


Organizer.

PART 8 · OUTPUT AND FILES


25. Reports and Compare Projects

Group	Reports
Dashboards	Project Overview, Cost Overview, Earned Value, Burndown, Cash Flow, Work Overview, Cost Overruns
Tasks	Critical Tasks, Task Status, Milestones, Late Tasks, Upcoming Tasks, Slipping Tasks
Resources	Resource Overview, Who Does What, Overallocated Resources

Reports open in a report window from which they can be printed or saved as PDF. **Custom Reports** opens the **report designer**: build your own report from text, key project figures, task tables (any fields, filtered), task bar charts of any numeric field, and resource tables.

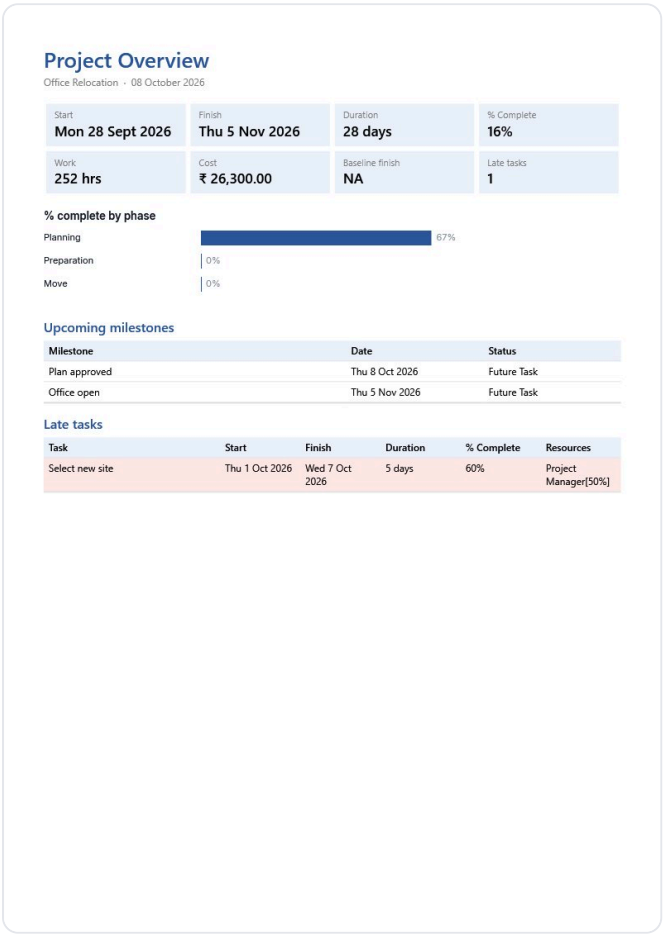

Project Overview report.

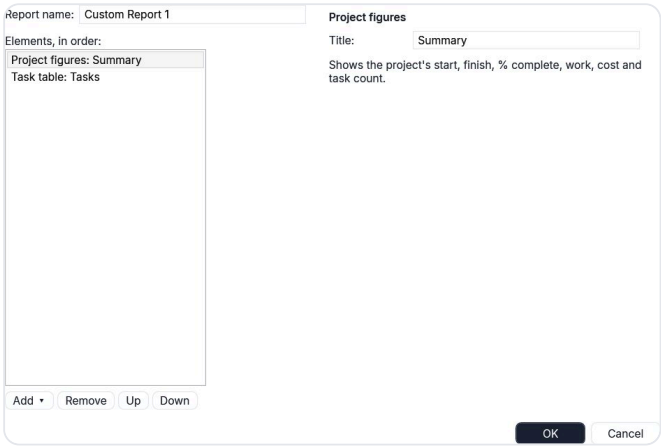


Report designer.

Compare Projects (**Report › Compare Projects**) opens an earlier version of the plan and lists tasks and resources that were added, removed or changed, field by field.


PART 8 · OUTPUT AND FILES

26. Printing, PDF and images

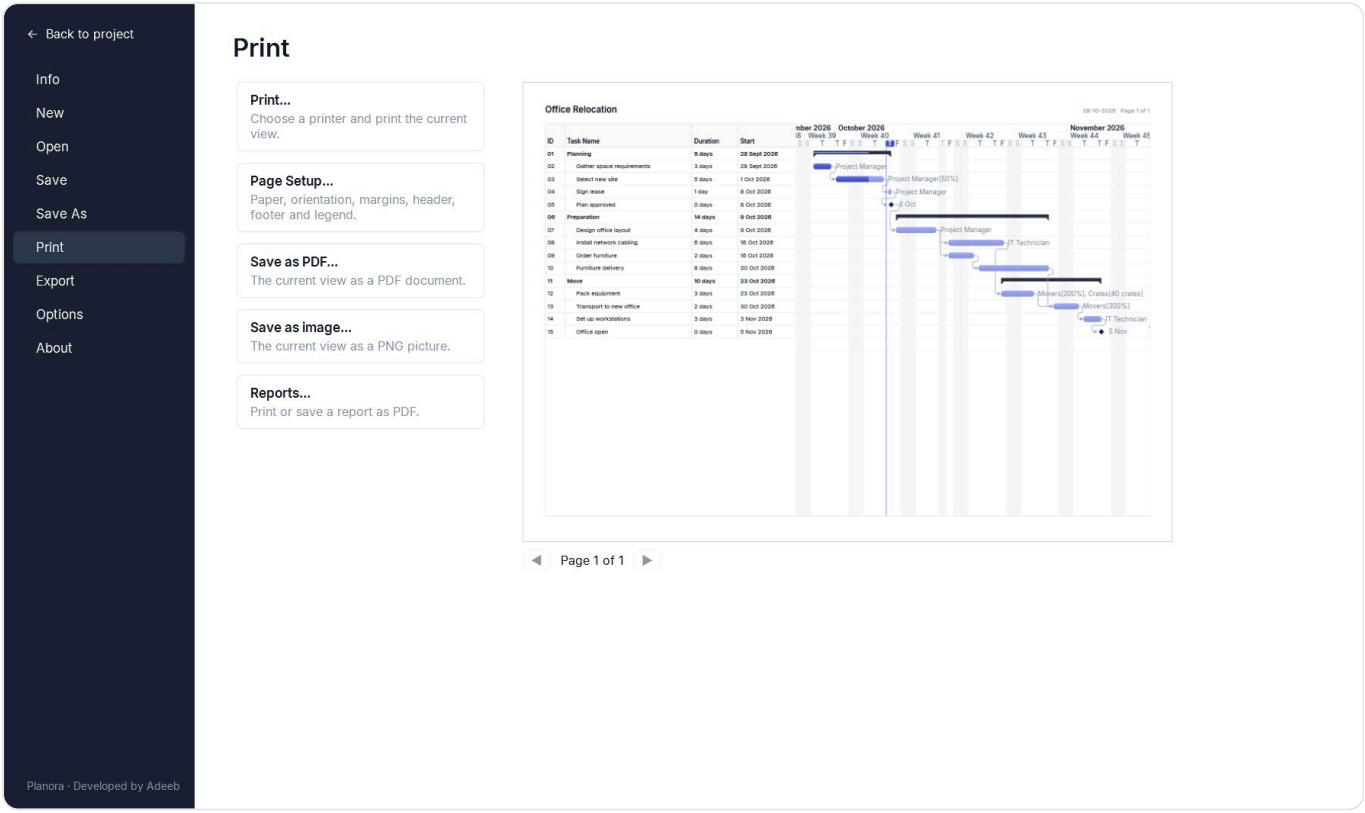

File › Print with page-by-page preview.

- **Page Setup**: paper size, orientation, margins, scaling, header and footer text (with project name, page number and date codes), and the Gantt legend.
- **Print** prints the current view; **Export as PDF** and **Export as Image** save it as a PDF document or PNG picture.

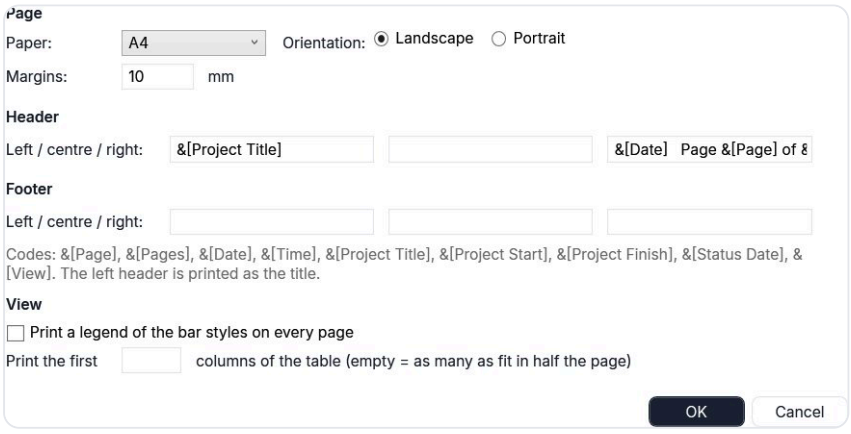


Page Setup.

PART 8 · OUTPUT AND FILES

27. Opening, importing and exporting

Format	Open	Save / export	Notes
Planora project (.planora)	Yes	Yes	Planora's own format: keeps everything.
Microsoft Project (.mpp, .mpt)	Yes	No	Opens .mpp files saved by current and older versions of Microsoft Project. To give a plan back to Microsoft Project, export Microsoft Project XML.
Microsoft Project XML (.xml)	Yes	Yes	Full schedule, resources, assignments, calendars, baselines, custom fields, splits and contours.
Excel (.xlsx) and CSV	Yes	Yes	Import Wizard maps your columns to Planora fields.
Primavera P6 (.xer, P6 XML)	Yes	Yes	
MPX (.mpx)	Yes	Yes	
Asta, Phoenix, GanttProject and others	Yes	No	.pp, .ppx, .gan, .sdef, .fts, .pod, .cdpx, .schedule_grid
Planora template	Yes	Yes	File › Save as Template; File › New › From a template.

When a file contains something Planora cannot bring in exactly (for example a link to a missing task), Planora opens it anyway and lists the **import notes**. Files opened from other formats open as new, unsaved Planora projects.

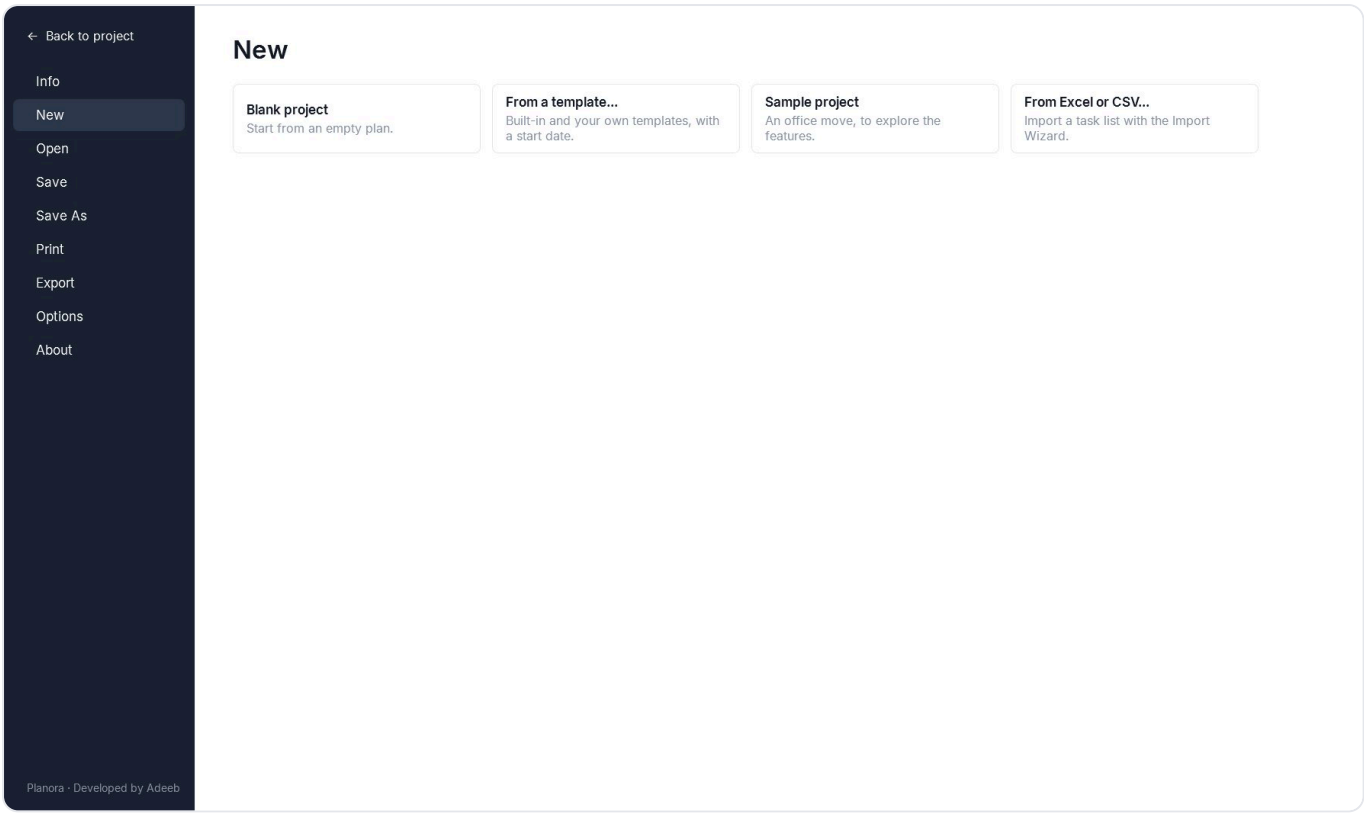

File › New: blank project, templates, sample project, or import from Excel/CSV.


PART 8 · OUTPUT AND FILES

28. Multiple projects and resource pools

- **Subprojects**: **Project › Insert Subproject** inserts another project file as a summary task; its tasks can be edited in place, refreshed from the file, and saved back to it. A project made of subprojects is a **master project**.
- **Links between projects**: **Project › Link to Other Project** makes a task in another file a predecessor; *Refresh External Links* re-reads its dates.
- **Resource pools**: **Resource › Share Resources** uses the resources of a pool file; *Refresh from Pool* and *Update Pool* keep them in step, and *Pool Overallocations* checks resources across every project that shares the pool.

29. Macros

View › Macros (`Alt` + `F8`) writes and runs macros in a VBA-like language: loops, conditions, variables and functions over tasks, resources and fields — for example to set a custom field on every critical task. Macros are saved with the project and can be copied with the Organizer.

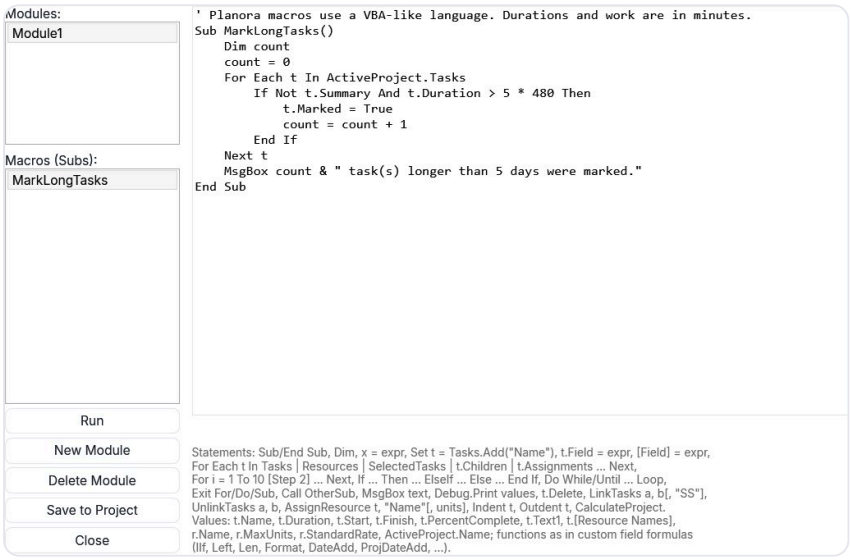


Macros.

> **Note.** Planora's macro language resembles VBA, but macros written for Microsoft Project's VBA object model do not run unchanged.

30. Options, autosave and recovery

- **File › Options**: whether new tasks are manually scheduled or effort driven, the default task type, the autosave interval and the accent colour.
- **Project Information**: start or finish date, status date, calendar, hours per day and week, days per month, critical slack, honour constraints and autolink.
- **Autosave** keeps a recovery copy of unsaved changes at the chosen interval. If Planora closes unexpectedly, it offers to recover your work the next time it starts.

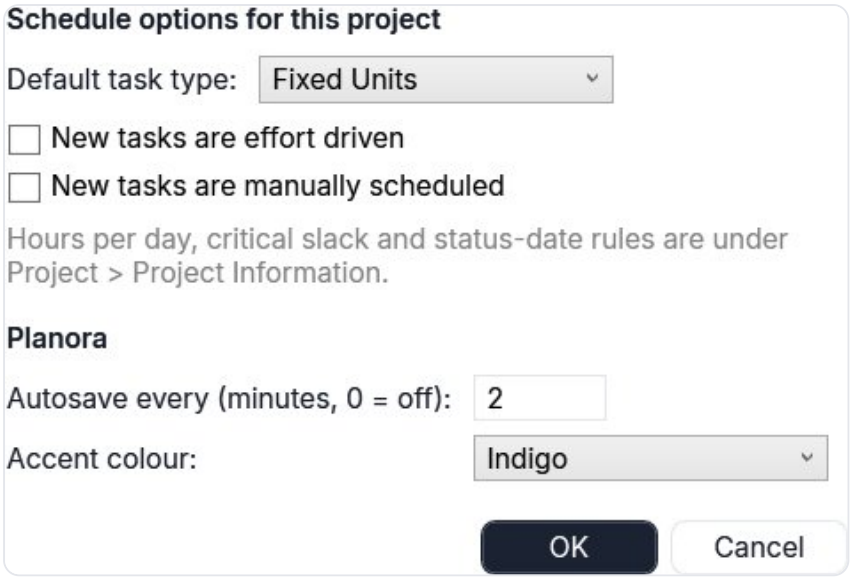
Schedule options for this project
Default task type:
Fixed Units
New tasks are effort driven
New tasks are manually scheduled
Hours per day, critical slack and status-date rules are under Project > Project Information.
Planora
Autosave every (minutes, 0 = off):
2
Accent colour:
Indigo
OK
Cancel

Options.

APPENDIX

A. Typing durations, dates and links

You type	Planora reads
`30m`, `4h`	30 minutes, 4 hours of working time
`5d`, `2w`, `1mo`	5 days, 2 weeks, 1 month of working time (lengths set in Project Information)
`3ed`, `1ew`	Elapsed: 3 calendar days, 1 calendar week
`4d?`	An estimated duration
`0d`	A milestone
`3`, `3FS+2d`, `5SS-1d`, `7FF+25%`	Predecessors with type and lag
`Movers[200%]`, `Crates[40]`	Resource names with units or quantities
`28 Sep 2026`, `28/09/2026 13:00`	Dates in your Windows format; a date without a time means the start of that working day (or its end, for finish dates)

B. Troubleshooting

Problem	What to do
A task will not move earlier	Select it and click **Inspect**: a predecessor, a constraint (perhaps set by dragging) or an actual start is holding it.
The finish date is later than expected	Turn on **Critical path**; shorten or overlap the red tasks, or add resources to effort-driven tasks.
A resource shows red	It is overallocated. Use Resource Usage to see when, then reassign work or run **Level Resources**.
Microsoft Project cannot open my file	Planora cannot write .mpp. Export **Microsoft Project XML** instead; Microsoft Project opens it and can save it as .mpp.
Setup shows “Windows protected your PC”	Click **More info › Run anyway**. The Setup file is not code-signed.
Planora closed unexpectedly	Start it again and accept the offer to recover the autosaved copy.

C. About Planora

Planora 1.0 is project scheduling and control software for Windows, **developed by Adeeb**. It reads Microsoft Project files with MPXJ and MPXJ.Net (LGPL 2.1) running on IKVM (MIT), and uses the Inter typeface (SIL Open Font License 1.1). See THIRD-PARTY-NOTICES.md in the program folder.

Microsoft and Microsoft Project are trademarks of Microsoft Corporation. Primavera is a trademark of Oracle. Planora is independent software and is not affiliated with or endorsed by Microsoft or Oracle.
